BRUHAT BANGALORE MAHANAGARA PALIKE

Name of Work:Improvements to Roads and drains works at Kattigenahalli Main and Cross, Sirinagara, Niranthara layout, SriKrishna Garden, ShivaShankar layout, Varaha layout, Bindu layout and Surrounding areas in Ward No-05

Measurement Sheet

First and Part Bill

Item No: **16** 9/11/2020 to 13/11/2020

Item Name: KSRRB M500-17. Providing and laying Dense Graded Bituminous Macadam using crushed aggregates of specified grading, premixed with VG30 grade bituminous binder and, transporting the hot mix to work site, laying to the required grade, level and alignment, rolling with smooth wheeled, vibratory and tandem rollers to achieve the desired compaction in all respects complete as per specifications. clause 505 of MORTH V revisionusing 40/60 TPH capacity H.M.P. with mechanical paver Gr-II (50mm to 70mm) with 4.5% VG-30 bitumen with all lead and lift and as per the

Premeasurement recorded on:

SLNO	CHAINAGE Land Mark		NO	L (m)	B (m)	B1 (m)	Avg B (m)	D (m)	QTY	REMARKS
	Kattigenahalli main road									
	0.00	30.00	1	30.00	10.00	10.50	10.25	0.050	15.38	
	30.00	60.00	1	30.00	10.50	10.70	10.60	0.050	15.90	
	60.00	90.00	1	30.00	10.70	10.70	10.70	0.050	16.05	
	90.00	120.00	1	30.00	10.70	10.80	10.75	0.050	16.13	
	120.00	150.00	1	30.00	10.80	10.10	10.45	0.050	15.68	
	150.00	180.00	1	30.00	10.10	9.70	9.90	0.050	14.85	
	180.00	210.00	1	30.00	9.70	9.10	9.40	0.050	14.10	
	210.00	240.00	1	30.00	9.10	9.30	9.20	0.050	13.80	
	240.00	270.00	1	30.00	9.30	7.10	8.20	0.050	12.30	
	270.00	300.00	1	30.00	7.10	6.90	7.00	0.050	10.50	
	300.00	330.00	1	30.00	6.90	6.50	6.70	0.050	10.05	
	330.00	350.00	1	20.00	6.50	13.00	9.75	0.050	9.75	
	350.00	370.00	1	20.00	13.00	7.60	10.30	0.050	10.30	
	370.00	390.00	1	20.00	7.60	7.00	7.30	0.050	7.30	
	390.00	420.00	1	30.00	7.00	6.80	6.90	0.050	10.35	
	420.00	450.00	1	30.00	6.80	10.00	8.40	0.050	12.60	
	450.00	480.00	1	30.00	10.00	7.00	8.50	0.050	12.75	
	480.00	510.00	1	30.00	7.00	8.50	7.75	0.050	11.63	
	510.00	540.00	1	30.00	8.50	8.10	8.30	0.050	12.45	
	540.00	551.00	1	11.00	6.20	12.80	9.50	0.050	5.23	
	551.00	564.00	1	13.00	15.60	12.60	14.10	0.050	9.17	
	564.00	580.00	1	16.00	12.60	9.40	11.00	0.050	8.80	
	580.00	604.00	1	24.00	9.40	9.00	9.20	0.050	11.04	
	Sri Krishna garden main road								0.00	
	0.00	30.00	1	30.00	7.40	7.40	7.40	0.050	11.10	
	30.00	60.00	1	30.00	7.40	7.45	7.43	0.050	11.14	
	60.00	90.00	1	30.00	7.45	7.20	7.33	0.050	10.99	
	90.00	120.00	1	30.00	7.20	7.30	7.25	0.050	10.88	
	120.00	150.00	1	30.00	7.30	7.30	7.30	0.050	10.95	

9/11/20 – 13/11/20

Scanned with CamScanner

SLNO	CHAINAGE Land Mark		NO	L (m)	B (m)	B1 (m)	Avg B (m)	D (m)	QTY	REMARKS
	150.00	180.00	1	30.00	7.30	7.00	7.15	0.050	10.73	
	180.00	210.00	1	30.00	7.00	6.90	6.95	0.050	10.43	
	210.00	213.00	1	3.00	6.90	6.90	6.90	0.050	1.04	
	Sri Krishna garden cross road A									
	0.00	30.00	1	30.00	7.50	7.00	7.25	0.050	10.88	
	30.00	60.00	1	30.00	7.00	7.70	7.35	0.050	11.03	
	Sri Krishna garden cross road B									
	0.00	30.00	1	30.00	5.80	7.20	6.50	0.050	9.75	
	30.00	60.50	1	30.50	7.20	7.20	7.20	0.050	10.98	
	Sri Krishna garden cross road C									
	0.00	30.00	1	30.00	5.60	6.00	5.80	0.050	8.70	
	30.00	57.80	1	27.80	6.00	5.50	5.75	0.050	7.99	
	Sri Krishna garden cross road D									
	0.00	30.00	1	30.00	5.20	5.80	5.50	0.050	8.25	
	30.00	56.80	1	26.80	5.80	5.80	5.80	0.050	7.77	
	Sri Krishna garden cross road E									
	0.00	30.00	1	30.00	5.30	6.10	5.70	0.050	8.55	
	30.00	53.00	1	23.00	6.10	5.90	6.00	0.050	6.90	
								Total Qty Work Done	**444.11**	**Cum**
								Qty Payable in this bill	**444.11**	**Cum**

NEWZEN CONSULTANT Bangalore

Contractor Representative

Consultant Representative

13/11/2020

Asst Engineer

Asst. Executive Engineer

13/11/2020

Asst Engineer

ಬ್ಯಾಟರಾಯನಪುರ ಉಪ ವಿಭಾಗ

ಬಿ.ಬಿ.ಎಂ.ಪಿ

Asst. Executive Engineer

ಬ್ಯಾಟರಾಯನಪುರ ಉಪ ವಿಭಾಗ

ಬಿ.ಬಿ.ಎಂ.ಪಿ., ಬೆಂಗಳೂರು-24

Scanned with CamScanner

Name of Work: Improvements to roads and drains at Kattigenahalli Main and Cross, Sirinagara Nirantara Layout, Sri krishna Garden, Shivashankara Layout, Varaha Layout, Bindhu Layout, and Surrounding areas in Ward No- 05

MEASUREMENT SHEETS

"FIRST AND PART BILL"

Scanned with CamScanner

BRUHAT BANGALORE MAHANAGARA PALIKE

Name of Work:Improvements to Roads and drains works at Kattigenahalli Main and Cross, Sirinagara, Niranthara layout, Sri Krishna Garden, ShivaShankar layout, Varaha layout, Bindu layout and Surrounding areas in Ward No-05

Measurement Sheet

First and Part Bill

Item No:	1									
Item Name:	Removing and Refixing stone slabs of drains and pointing in C.M(1:3) with all lead and lift and as per the directioon of Engineer in -charge									
SLNO	CHAINAGE Land Mark	NO	L (m)	B (m)	D (m)	QTY	REMARKS	RATE	AMOUNT
	Vide Premeasurement Page no.					1646.40			
					Qty Payable in this bill	**1646.40**	**Sqm**	**116.00**	**190982.40**

Item No:	2									
Item Name:	KSRRB300 - Excavation for road, drains and similar works ,KSRRB300-1 : Earthwork excavation by manual means in ordinary soil involving as average horizontal throw upto 2 mters and an average lifts upto 0.5m, excavated surface leveled and sides neatly dressed, the disposed earth to be leveled neatly after									
SLNO	CHAINAGE Land Mark	NO	L (m)	B (m)	D (m)	QTY	REMARKS	RATE	AMOUNT
	Vide Premeasurement Page no.					1058.05			
					Qty Payable in this bill	**1058.05**	**Cum**	**217.00**	**229597.07**

Item No:	3									
Item Name:	providng granite slabs of selecting quality roughly dressed having a size of 7.5 cms thick and fixed in cement mortar (1:6) including fixing curing etc., complete with all lead and lifts and as per the direction of Engineer in-charge.									
SLNO	CHAINAGE Land Mark	NO	L (m)	B (m)	D (m)	QTY	REMARKS	RATE	AMOUNT
	Vide Premeasurement Page no.					2008.80			
					Qty Payable in this bill	**2008.80**	**Sqm**	**779.00**	**1564855.20**

Item No:	4									
Item Name:	KSRB M2100-10 : Providing and laying plain cement concrete of Mix 1:3:6 with OPC @ 220kgs,with crushed 40mm and down size graded granite mental coarse aggregate @ 0.89 cum and fine aggregate @ 0.46 cum, in foundation mechanically mixed , placed in foundation and compacted by vibration including curing for 14									
SLNO	CHAINAGE Land Mark	NO	L (m)	B (m)	D (m)	QTY	REMARKS	RATE	AMOUNT
	Vide Premeasurement Page no.					8.42			
					Qty Payable in this bill	**8.42**	**Cum**	**5692.00**	**47949.41**

ಸಹಾಯಕ ಅಭಿಯಂತರರು
ಬಿ.ಬಿ.ಎಂ.ಪಿ ಬ್ಯಾಟರಾಯನಪುರ ಉಪ ವಿಭಾಗ

ಸಹಾಯಕ ಅಭಿಯಂತರರು
ಬ್ಯಾಟರಾಯನಪುರ ಉಪ ವಿಭಾಗ
ಬಿ.ಬಿ.ಎಂ.ಪಿ., ಬೆಂಗಳೂರು-24

Scanned with CamScanner

SLNO	CHAINAGE / Land Mark	NO	L (m)	B (m)	D (m)	QTY	REMARKS	RATE	AMOUNT
Item No:	5								
Item Name:	KSRB 5.2-3: Providing and constructing granite / trap / basit size stone masonary in foundation with cement mortar, stone hammered dressed in course not less then 20 cms high, bond stones at 2m, apart in each course including cost materials, labour, curing complete as per specifications. KBS 5.1.13,cement mortar 1:6 KBS 5.1.13								
SLNO	CHAINAGE / Land Mark	NO	L (m)	B (m)	D (m)	QTY	REMARKS	RATE	AMOUNT
	Vide Premeasurement Page no.					22.46			
	Qty Payable in this bill					**22.46**	**Cum**	**5114.00**	**114880.90**
Item No:	6								
Item Name:	KSRB 4-1.6: Providing and laying in position plain cement concrete of Mix 1:2:4 with OPC at 240kgs, with 20mm and down size granite metal coarse aggregates at 0.878 cum and fine aggregates at 0.53cum machine mixed, concrete laid in layers not exceeding 15cms. thick, well compacted, in foundations, plinth and cills,								
SLNO	CHAINAGE / Land Mark	NO	L (m)	B (m)	D (m)	QTY	REMARKS	RATE	AMOUNT
	Vide Premeasurement Page no.					458.36			
	Qty Payable in this bill					**458.36**	**Cum**	**6034.00**	**2765732.17**
Item No:	7								
Item Name:	KSRB 5-14: providing and contructing load bearing wall with solid concrete blocks of size 400*150*200mm having block density not lessthen 1800kg/m3 and having a minimum average compressive strength 4.00 N/mm2 confirming to IS 2185(part):2005 and constructed with 1:4 , as per IS 2572:2005 including cost of all								
SLNO	CHAINAGE / Land Mark	NO	L (m)	B (m)	D (m)	QTY	REMARKS	RATE	AMOUNT
	Vide Premeasurement Page no.					3535.52			
	Qty Payable in this bill					**3535.52**	**Sqm**	**1028.00**	**3634514.56**

NEWZEN CONSULTANT ★ Bangalore ★

Contractor Representative

Consultant Representative

Asst Engineer

Asst.Executive Engineer

Scanned with CamScanner

BRUHAT BANGALORE MAHANAGARA PALIKE

Name of Work:Improvements to Roads and drains works at Kattigenahalli Main and Cross, Sirinagara, Niranthara layout, SriKrishna Garden, ShivaShankar layout, Varaha layout, Bindu layout and Surrounding areas in Ward No-05

Measurement Sheet

First and Part Bill

Item No: 8 | 14/10/2020 to 04/11/2020

Item Name: Providing and Fixing RCC pre cast covering Slab of 100mm thick for drains in cement concrete M25 using graded granite jelly 20mm and down size with steel reinforecement , inclunding form work, lift charges, curing and concrete finishined surfaces on both side etc., complete as per drawing and the directions of Engineer in-charge.(Date rate)

Measurement recorded on:

SLNO	CHAINAGE Land Mark		NO	L (m)	B (m)	BI (m)	Avg B (m)	D (m)	QTY	REMARKS	RATE	AMOUNT
	Bindu Layout RHS (1st cross road)											
	0.00	30.00	1	30.00	0.75				22.50			
	30.00	36.00	1	6.00	0.75				4.50			
	36.00	45.30	1	9.30	0.90					bs slab		
	45.30	54.50	1	9.20	0.75				6.90			
	54.50	63.60	1	9.10	0.90					bs slab		
	63.60	81.80	1	18.20	0.75				13.65			
	Bindu Layout LHS (1st cross road)											
	0.00	14.10	1	14.10	0.75				10.58			
	14.10	23.30	1	9.20	0.75				6.90			
	23.30	32.80	1	9.50	0.90					bs slab		
	32.80	62.80	1	30.00	0.75				22.50			
	62.80	69.80	1	7.00	0.75				5.25			
	69.80	79.00	1	9.20	0.90					bs slab		
	79.00	91.90	1	12.90	0.75				9.68			
	Bindu layout LHS (2 nd cross road)											
	0.00	28.30	1	28.30	0.75				21.23			
	28.30	30.30	1	2.00	0.90					bs slab		
	30.30	60.30	1	30.00	0.75				22.50			
	60.30	87.30	1	27.00	0.75				20.25			
	Bindu layout RHS (2 nd cross road)								22.50			
	0.00	30.00	1	30.00	0.75				12.38			
	30.00	46.50	1	16.50	0.75					bs slab		
	46.50	52.20	1	5.70	0.90				22.50			
	52.20	82.20	1	30.00	0.75				3.15			
	82.20	86.40	1	4.20	0.75							
	Bindu layout RHS (3rd cross road)								22.50			
	0.00	30.00	1	30.00	0.75				22.50			
	30.00	60.00	1	30.00	0.75				4.95			
	60.00	66.60	1	6.60	0.75							
	Bindu layout LHS (3rd cross road)								7.13			
	0.00	9.50	1	9.50	0.75					bs slab		
	9.50	18.10	1	8.60	0.90				22.50			
	18.10	48.10	1	30.00	0.75				13.58			
	48.10	66.20	1	18.10	0.75							
	Varaha Layout LHS (1st cross road)								27.00			
	0.00	30.00	1	30.00	0.90				2.79			
	30.00	33.10	1	3.10	0.90					Cross road		
	33.10	42.30	1	9.20					28.68			
	42.30	66.20	1	23.90	1.20				19.53			
	66.20	87.90	1	21.70	0.90				22.50			
	87.90	112.90	1	25.00	0.90							

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಬ್ಯಾಟರಾಯನಪುರ ಉಪ ವಿಭಾಗ
ಬಿ.ಬಿ.ಎಂ.ಪಿ., ಬೆಂಗಳೂರು-24

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಬ್ಯಾಟರಾಯನಪುರ ಉಪ ವಿಭಾಗ
ಬಿ.ಬಿ.ಎಂ.ಪಿ., ಬೆಂಗಳೂರು-24

Scanned with CamScanner

SLNO	CHAINAGE Land Mark		NO	L (m)	B (m)	B1 (m)	Avg B (m)	D (m)	QTY	REMARKS	RATE	AMOUNT
	112.90	120.50	1	7.60	0.90				6.84			
	120.50	130.50	1	10.00						Cross road		
	130.50	141.60	1	11.10	1.20				13.32			
	141.60	154.80	1	13.20	0.90				11.88			
	154.80	163.30	1	8.50						Cross road		
	163.30	186.20	1	22.90	1.20				27.48			
	Varaha Layout RHS (1st cross road)											
	0.00	30.00	1	30.00	0.90				27.00			
	30.00	35.90	1	5.90	0.90				5.31			
	35.90	50.80	1	14.90	1.20				17.88			
	50.80	53.30	1	2.50	0.90				2.25			
	53.30	58.90	1	5.60						No work		
	58.90	67.80	1	8.90	0.90				8.01			
	67.80	72.10	1	4.30	1.20				5.16			
	72.10	98.40	1	26.30	0.90				23.67			
	98.40	127.00	1	28.60	0.90				25.74			
	127.00	150.00	1	23.00	1.20				27.60			
	150.00	160.90	1	10.90	0.90				9.81			
	Varaha Layout LHS (2nd cross road)											
	0.00	26.50	1	26.50	0.90				23.85			
	26.50	35.50	1	9.00	0.90					Bs slab		
	35.50	44.50	1	9.00	0.90				8.10			
	44.50	74.50	1	30.00	0.90					Bs slab		
	74.50	80.50	1	6.00	0.90					Bs slab		
	80.50	94.50	1	14.00	0.90				12.60			
	94.50	111.20	1	16.70	1.20					Bs slab		
	111.20	116.50	1	5.30	0.90				4.77			
	Varaha Layout RHS (2nd cross road)											
	0.00	30.00	1	30.00	0.90				27.00			
	30.00	54.00	1	24.00	0.90				21.60			
	54.00	84.00	1	30.00	0.90					Bs slab		
	84.00	114.00	1	30.00	1.20					Bs slab		
	114.00	117.80	1	3.80	1.20					Bs slab		
	Varaha Layout LHS (3 rd cross road)											
	0.00	9.00	1	9.00	0.90							
	9.00	18.80	1	9.80	0.90					Bs slab		
	18.80	45.40	1	26.60	0.90				23.94			
	45.40	55.00	1	9.60	0.90					Bs slab		
	55.00	85.00	1	30.00	0.90				27.00			
	85.00	115.00	1	30.00	0.90				27.00			
	115.00	118.80	1	3.80	0.90				3.42			
	Varaha Layout RHS (3 rd cross road)											
	0.00	22.90	1	22.90	0.90				20.61			
	22.90	26.90	1	4.00	1.20					Bs slab		
	26.90	45.20	1	18.30	0.90				16.47			
	45.20	54.50	1	9.30	1.20					Bs slab		
	54.50	63.30	1	8.80	0.90				7.92			
	63.30	82.20	1	18.90	1.20					Bs slab		
	82.20	91.70	1	9.50	0.90				8.55			
	91.70	100.70	1	9.00	0.90					Bs slab		
	100.70	118.50	1	17.80	0.90				16.02			
	Varaha Layout LHS (4th cross road)											
	0.00	8.40	1	8.40	0.90				7.56			
	8.40	17.50	1	9.10	0.90					Bs slab		

Scanned with CamScanner

SLNO	CHAINAGE		NO	L	B	Bl	Avg B	D	QTY	REMARKS	RATE	AMOUNT
	Land Mark			(m)	(m)	(m)	(m)	(m)				
	17.50	47.50	1	30.00	0.90				27.00			
	47.50	72.50	1	25.00	0.90				22.50			
	72.50	76.50	1	4.00	0.90					Bs slab		
	76.50	81.70	1	5.20	0.90				4.68			
	81.70	111.70	1	30.00	0.90				27.00			
	111.70	117.20	1	5.50								
	Varaha Layout RHS (4th cross road)											
	0.00	17.50	1	17.50	0.90				15.75			
	17.50	27.50	1	10.00	1.20					Bs slab		
	27.50	36.30	1	8.80	0.90				7.92			
	36.30	45.30	1	9.00	1.00					Bs slab		
	45.30	63.80	1	18.50	0.90				16.65			
	63.80	93.80	1	30.00	1.20					Bs slab		
	93.80	100.00	1	6.20	1.20					Bs slab		
	100.00	117.80	1	17.80	0.90				16.02			
	Varaha Layout RHS (5th cross road)											
	0.00	30.00	1	30.00	0.90				27.00			
	30.00	47.70	1	17.70	0.90				15.93			
	47.70	56.90	1	9.20	0.90					Bs slab		
	56.90	66.00	1	9.10	0.90				8.19			
	66.00	93.50	1	27.50	0.90					Bs slab		
	93.50	103.50	1	10.00	0.90				9.00			
	Varaha Layout RHS (5th cross road)											
	0.00	15.40	1	15.40	0.90				13.86			
	15.40	25.10	1	9.70						Cross road		
	25.10	47.70	1	22.60	0.90				20.34			
	47.70	57.40	1	9.70						Cross road		
	57.40	80.30	1	22.90	0.90				20.61			
	80.30	90.20	1	9.90						Cross road		
	90.20	102.20	1	12.00	0.90				10.80			
	Varaha Layout LHS (6th cross road)											
	0.00	10.70	1	10.70	0.90				9.63			
	10.70	18.40	1	7.70	0.75				5.78			
	18.40	21.50	1	3.10	0.90				2.79			
	21.50	31.90	1	10.40	0.75				7.80			
	Shivashankar Layout LHS (1st cross road)											
	0.00	14.00	1	14.00	0.90				12.60			
	14.00	44.00	1	30.00	0.90					Bs Slab		
	44.00	57.30	1	13.30	1.20					Bs Slab		
	57.30	87.30	1	30.00	0.90				27.00			
	87.30	117.30	1	30.00	0.90				27.00			
	117.30	133.30	1	16.00	0.90				14.40			
	133.30	139.80	1	6.50	0.90					old slab		
	139.80	168.80	1	29.00	0.90				26.10			
	Shivashankar Layout RHS (1st cross road)											
	0.00	15.00	1	15.00	0.90				13.50			
	15.00	42.00	1	27.00	0.90					Bs Slab		
	42.00	51.00	1	9.00	0.90				8.10			
	51.00	81.00	1	30.00	0.90					old slab		
	81.00	87.60	1	6.60	0.90					old slab		
	87.60	117.60	1	30.00	0.90				27.00			
	117.60	129.60	1	12.00	0.90				10.80			

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಬ್ಯಾಟರಾಯನಪುರ ಉಪ ವಿಭಾಗ
ಬಿ.ಬಿ.ಎಂ.ಪಿ., ಬೆಂಗಳೂರು-24

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಬ್ಯಾಟರಾಯನಪುರ ಉಪ ವಿಭಾಗ
ಬಿ.ಬಿ.ಎಂ.ಪಿ., ಬೆಂಗಳೂರು-24

Scanned with CamScanner

SLNO	CHAINAGE Land Mark		NO	L (m)	B (m)	Bl (m)	Avg B (m)	D (m)	QTY	REMARKS	RATE	AMOUNT
	129.60	162.60	1	33.00	0.90					Bs Slab		
	Shivashankar Layout LHS (2nd cross road)											
	0.00	30.00	1	30.00	0.90				27.00			
	30.00	60.00	1	30.00	0.90				27.00			
	60.00	80.00	1	20.00	0.90				18.00			
	80.00	83.00	1	3.00	0.90					old slab		
	83.00	103.50	1	20.50	0.90				18.45			
	103.50	108.10	1	4.60	0.90					old slab		
	108.10	138.10	1	30.00	0.90				27.00			
	138.10	168.10	1	30.00	0.90				27.00			
	168.10	171.70	1	3.60	0.90				3.24			
	Shivashankar Layout RHS (2nd cross road)											
	0.00	21.60	1	21.60	0.90				19.44			
	21.60	26.40	1	4.80	0.90					Bs Slab		
	26.40	35.80	1	9.40	0.90				8.46			
	35.80	45.20	1	9.40	0.90					Bs Slab		
	45.20	54.00	1	8.80	0.90				7.92			
	54.00	65.00	1	11.00	1.20					Bs Slab		
	65.00	72.40	1	7.40	0.90				6.66			
	72.40	87.60	1	15.20	0.90				13.68			
	87.60	97.20	1	9.60	0.90					Bs Slab		
	97.20	115.60	1	18.40	0.90				16.56			
	115.60	145.60	1	30.00	0.90				27.00			
	145.60	149.30	1	3.70	1.20					Bs Slab		
	149.30	171.00	1	21.70	0.90				19.53			
	Shivashankar Layout LHS (3rd cross road)											
	0.00	16.40	1	16.40	0.90				14.76			
	16.40	22.40	1	6.00	0.90				5.40			
	22.40	52.40	1	30.00	0.90				27.00			
	52.40	80.90	1	28.50	0.90				25.65			
	80.90	90.20	1	9.30	0.90					Bs Slab		
	90.20	99.50	1	9.30	0.90					Bs Slab		
	99.50	126.80	1	27.30	0.90				24.57			
	126.80	145.50	1	18.70	1.00					Bs Slab		
	145.50	155.50	1	10.00	0.90				9.00			
	Shivashankar Layout RHS (3rd cross road)											
	0.00	16.70	1	16.70	0.90				15.03			
	16.70	26.00	1	9.30	0.90					Bs Slab		
	26.00	44.30	1	18.30	0.90				16.47			
	44.30	53.80	1	9.50	0.90					Bs Slab		
	53.80	83.80	1	30.00	0.90				27.00			
	83.80	113.80	1	30.00	0.90				27.00			
	113.80	118.30	1	4.50	0.90				4.05			
	118.30	121.90	1	3.60	0.90					old slab		
	121.90	127.50	1	5.60	0.90				5.04			
	127.50	157.50	1	30.00	0.90				27.00			
	157.50	160.50	1	3.00	0.90				2.70			
	Shivashankar Layout LHS (4th cross road)											
	0.00	26.30	1	26.30	0.90				23.67			
	26.30	56.30	1	30.00	1.20					Bs Slab		

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಬ್ಯಾಟರಾಯನಪುರ ಉಪ ವಿಭಾಗ
ಬಿ.ಬಿ.ಎಂ.ಪಿ. ಬ್ಯಾಟರಾಯನಪುರ ಉಪ ವಿಭಾಗ

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಬ್ಯಾಟರಾಯನಪುರ ಉಪ ವಿಭಾಗ
ಬಿ.ಬಿ.ಎಂ.ಪಿ. ಬೆಂಗಳೂರು-26

Scanned with CamScanner

SLNO	CHAINAGE Land Mark		NO	L (m)	B (m)	BI (m)	Avg B (m)	D (m)	QTY	REMARKS	RATE	AMOUNT
	56.30	63.30	1	7.00	1.20					Bs Slab		
	63.30	90.80	1	27.50	0.90				24.75			
	90.80	119.20	1	28.40	1.20					Bs Slab		
	119.20	126.90	1	7.70	0.90				6.93			
	126.90	136.90	1	10.00	0.90					Bs Slab		
	136.90	168.90	1	32.00	0.90				28.80			
	168.90	184.90	1	16.00	0.90					Bs Slab		
	184.90	201.40	1	16.50	0.90				14.85			
	Shivashankar Layout RHS (4th cross road)											
	0.00	29.00	1	29.00	0.90				26.10			
	29.00	59.00	1	30.00	0.90				27.00			
	59.00	71.00	1	12.00	0.90				10.80			
	71.00	75.80	1	4.80	0.90				4.32			
	75.80	80.20	1	4.40	0.90					old slab		
	80.20	85.00	1	4.80	0.90				4.32			
	85.00	89.50	1	4.50	0.90					Bs Slab		
	89.50	94.00	1	4.50	0.90				4.05			
	94.00	103.20	1	9.20	1.20					Bs Slab		
	103.20	121.20	1	18.00	0.90				16.20			
	121.20	139.90	1	18.70	0.90					Bs Slab		
	139.90	169.90	1	30.00	0.90				27.00			
	169.90	184.70	1	14.80	0.90				13.32			
	Kattigenahalli LHS (1 st cross road)											
	0.00	4.80	1	4.80	0.90				4.32			
	4.80	6.40	1	1.60	0.90					Bs slab		
	6.40	28.40	1	22.00	0.90				19.80			
	28.40	36.90	1	8.50	0.90					Bs slab		
	36.90	65.10	1	28.20	0.90				25.38			
	65.10	67.80	1	2.70	0.90					Bs slab		
	67.80	92.10	1	24.30	0.90				21.87			
	92.10	94.10	1	2.00	0.90					Bs slab		
	94.10	103.50	1	9.40	0.90				8.46			
	103.50	111.00	1	7.50	0.90					Bs slab		
	111.00	121.40	1	10.40	0.90				9.36			
	Kattigenahalli RHS (1 st cross road)											
	0.00	8.50	1	8.50						No work		
	8.50	15.70	1	7.20	0.90				6.48			
	15.70	21.20	1	5.50	0.90					Bs slab		
	21.20	51.70	1	30.50	0.90				27.45			
	51.70	57.70	1	6.00	0.90					Bs slab		
	57.70	64.70	1	7.00	0.90				6.30			
	64.70	72.70	1	8.00	0.90					Bs slab		
	72.70	102.70	1	30.00	0.90				27.00			
	102.70	112.50	1	9.80	0.90				8.82			
	112.50	114.50	1	2.00	0.90					Bs slab		
	114.50	124.50	1	10.00	0.90				9.00			
	Kattigenahalli LHS (2 nd cross road)											
	0.00	26.60	1	26.60	0.90				23.94			
	26.60	32.60	1	6.00						culvert		
	32.60	44.60	1	12.00	0.90					Bs slab		
	44.60	56.20	1	11.60	0.90				10.44			
	56.20	62.20	1	6.00	0.90					Bs slab		
	62.20	67.90	1	5.70	0.90				5.13			
	67.90	79.70	1	11.80	1.00					Bs slab		

Scanned with CamScanner

SLNO	CHAINAGE		NO	L	B	BI	Avg B	D	QTY	REMARKS	RATE	AMOUNT
	Land Mark			(m)	(m)	(m)	(m)	(m)				
	79.70	91.90	1	12.20	0.90				10.98			
	91.90	97.20	1	5.30	0.90					Bs slab		
	97.20	98.40	1	1.20	0.90				1.08			
	Kattigenahalli RHS (2 nd cross road)											
	0.00	20.90	1	20.90	0.90				18.81			
	20.90	33.30	1	12.40	1.20					Bs slab		
	33.30	56.70	1	23.40	0.90				21.06			
	56.70	62.90	1	6.20	0.90					Bs slab		
	62.90	93.60	1	30.70	0.90				27.63			
	93.60	96.20	1	2.60	0.90					Bs slab		
	96.20	123.00	1	26.80	0.90				24.12			
	Srinagar LHS (cross road)											
	0.00	20.00	1	20.00	0.90				18.00			
	20.00	22.80	1	2.80	0.90				0.00	bs slab		
	22.80	30.20	1	7.40	0.90				6.66			
	30.20	39.40	1	9.20	0.90					cross road		
	39.40	51.60	1	12.20	0.90				10.98			
	51.60	63.90	1	12.30	0.90				11.07			
	Srinagar RHS (cross road)											
	0.00	30.00	1	30.00	0.90				27.00			
	30.00	45.00	1	15.00	0.90				13.50			
	Srinagar LHS (1 st cross road)											
	0.00	4.20	1	4.20	0.90				3.78			
	4.20	18.20	1	14.00	0.75				10.50			
	18.20	23.20	1	5.00	0.75				0.00	bs slab		
	23.20	53.20	1	30.00	0.90				27.00			
	53.20	82.40	1	29.20	0.90				26.28			
	82.40	84.20	1	1.80	1.20				2.16	bs slab		
	84.20	114.20	1	30.00	0.90				27.00			
	114.20	127.90	1	13.70	0.90				12.33			
	Srinagar RHS (1 st cross road)											
	0.00	7.30	1	7.30	0.90				6.57			
	7.30	9.10	1	1.80	1.20				0.00	bs slab		
	9.10	39.10	1	30.00	0.90				27.00			
	39.10	59.50	1	20.40	0.90				18.36			
	59.50	61.90	1	2.40	0.90				0.00	bs slab		
	61.90	68.80	1	6.90	0.90				6.21			
	68.80	73.20	1	4.40	0.90				0.00	bs slab		
	73.20	103.20	1	30.00	0.90				27.00			
	103.20	116.70	1	13.50	0.90				12.15			
	116.70	119.20	1	2.50	0.90				0.00	bs slab		
	119.20	124.30	1	5.10	0.90				4.59			
	124.30	128.30	1	4.00	0.90				0.00	bs slab		
	128.30	137.30	1	9.00	0.90				8.10			
	Srinagar LHS (2nd cross road)											
	0.00	14.80	1	14.80	0.90				13.32			
	14.80	20.30	1	5.50	0.90					cross road		
	20.30	48.60	1	28.30	0.90				25.47			
	48.60	51.50	1	2.90	0.90				0.00	bs slab		
	51.50	57.70	1	6.20	0.90				5.58			
	57.70	66.70	1	9.00	0.90				0.00	bs slab		
	66.70	84.90	1	18.20	0.90				16.38			
	84.90	93.90	1	9.00	0.90				0.00	bs slab		
	93.90	123.90	1	30.00	0.90				27.00			

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಬಿ.ಬಿ.ಎಂ.ಪಿ. ಬ್ಯಾಟರಾಯನಪುರ ಉಪ ವಿಭಾಗ

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಬ್ಯಾಟರಾಯನಪುರ ಉಪ ವಿಭಾಗ
ಬಿ.ಬಿ.ಎಂ.ಪಿ. ಬೆಂಗಳೂರು-24

Scanned with CamScanner

SLNO	CHAINAGE		NO	L	B	BI	Avg B	D	QTY	REMARKS	RATE	AMOUNT
	Land Mark			(m)	(m)	(m)	(m)	(m)				
	123.90	153.90	1	30.00	0.90				27.00			
	153.90	183.90	1	30.00	0.90				27.00			
	183.90	187.00	1	3.10	0.90				2.79			
	Srinagar RHS (2nd cross road)											
	0.00	30.00	1	30.00	0.90				27.00			
	30.00	35.40	1	5.40	0.90				4.86			
	35.40	41.00	1	5.60	0.90				0.00	bs slab		
	41.00	53.40	1	12.40	0.90				11.16			
	53.40	55.20	1	1.80	0.90				0.00	bs slab		
	55.20	73.90	1	18.70	0.90				16.83			
	73.90	83.20	1	9.30	0.90				0.00	bs slab		
	83.20	113.20	1	30.00	0.90				27.00			
	113.20	137.60	1	24.40	0.90				21.96			
	137.60	146.80	1	9.20	0.90				8.28			
	146.80	155.80	1	9.00	0.90				8.10			
	155.80	159.80	1	4.00	0.90				0.00	bs slab		
	159.80	186.80	1	27.00	0.90				24.30			
	Alpha School Road 1 LHS											
	0.00	4.50	1	4.50	0.90				4.05			
	4.50	7.50	1	3.00	0.90				2.70			
	7.50	13.50	1	6.00	0.90					bs slab		
	13.50	22.60	1	9.10	0.90				8.19			
	22.60	41.10	1	18.50	0.75					bs slab		
	41.10	69.60	1	28.50	0.90				25.65			
	Alpha School Road 1 RHS											
	0.00	13.40	1	13.40	0.90				12.06			
	13.40	19.10	1	5.70						cross road		
	19.10	29.10	1	10.00	0.90				9.00			
	29.10	33.90	1	4.80	0.90					bs slab		
	33.90	38.40	1	4.50	0.90				4.05			
	38.40	48.00	1	9.60	0.90					bs slab		
	48.00	62.30	1	14.30	0.90					bs slab		
	62.30	70.80	1	8.50	0.90				7.65			
	Alpha School Road 2 LHS											
	0.00	12.20	1	12.20	0.90				10.98			
	12.20	42.20	1	30.00	0.90					bs slab		
	42.20	49.20	1	7.00	0.90					bs slab		
	49.20	57.70	1	8.50	0.90				7.65			
	57.70	67.50	1	9.80	0.90					bs slab		
	Alpha School Road 2 RHS											
	0.00	21.50	1	21.50	0.90				19.35			
	21.50	27.20	1	5.70						Cross road		
	27.20	52.60	1	25.40	0.90				22.86			
	Alpha School Road 3 LHS											
	0.00	30.00	1	30.00	0.90				27.00			
	30.00	31.30	1	1.30	0.90				1.17			
	Alpha School Road 3 RHS											
	0.00	9.20	1	9.20	0.90				8.28			
	9.20	18.20	1	9.00	0.90					bs slab		
	18.20	28.70	1	10.50	0.90				9.45			
	28.70	31.30	1	2.60	0.90					bs slab		
	31.30	35.70	1	4.40	0.90				3.96			
	Sri Krishna Garden Main road RHS											

ಸಹಾಯಕ ಅಭಿಯಂತರರು
ಬಿ.ಬಿ.ಎಂ.ಪಿ ಬ್ಯಾಟರಾಯನಪುರ ಉಪ ವಿಭಾಗ.

ಸಹಾಯಕ ಅಭಿಯಂತರರು
ಬ್ಯಾಟರಾಯನಪುರ ಉಪ ವಿಭಾಗ
ಬಿ.ಬಿ.ಎಂ.ಪಿ, ಬೆಂಗಳೂರು-24

Scanned with CamScanner

SLNO	CHAINAGE Land Mark		NO	L (m)	B (m)	B1 (m)	Avg B (m)	D (m)	QTY	REMARKS	RATE	AMOUNT
	0.00	30.00	1	30.00	0.90				27.00			
	30.00	60.00	1	30.00	0.90				27.00			
	60.00	62.00	1	2.00	0.90				1.80			
	62.00	69.50	1	7.50						culvert		
	69.50	87.60	1	18.10	0.90				16.29			
	87.60	107.60	1	20.00	0.90					bs slab		
	107.60	114.60	1	7.00						culvert		
	114.60	128.00	1	13.40	0.90					cc slab		
	128.00	140.40	1	12.40	0.90				11.16			
	140.40	147.40	1	7.00						culvert		
	147.40	172.60	1	25.20	0.90				22.68			
	172.60	178.10	1	5.50						culvert		
	178.10	205.10	1	27.00	0.90					bs slab		
	205.10	217.10	1	12.00	0.90					bs slab		
	217.10	221.10	1	4.00	0.90				3.60			
	221.10	233.10	1	12.00	0.90					bs slab		
	233.10	242.10	1	9.00	0.90				8.10			
	242.10	251.10	1	9.00	0.90					bs slab		
	251.10	261.50	1	10.40	0.90					bs slab		
	Sri Krishna Garden Main road LHS				0.90							
	0.00	20.50	1	20.50	0.90				18.45			
	20.50	47.50	1	27.00	0.90				0.00	bs slab		
	47.50	55.30	1	7.80	0.90				7.02			
	55.30	85.30	1	30.00	0.90				27.00			
	85.30	115.30	1	30.00	0.90				27.00			
	115.30	145.30	1	30.00	0.90				27.00			
	145.30	175.30	1	30.00	0.90				27.00			
	175.30	205.30	1	30.00	0.90				27.00			
	205.30	235.30	1	30.00	0.90				27.00			
	235.30	237.70	1	2.40	0.90				0.00	bs slab		
	237.70	267.70	1	30.00	0.90				27.00			
	267.70	272.70	1	5.00	0.90				4.50			
								Total Qty Work Done	**3520.88**	**Sqm**		
								Qty Payable in this bill	**3520.88**	**Sqm**	**2453.00**	**8636706.38**

NEWZEN CONSULTANT ★ Bangalore ★

Consultant Representative

Contractor Representative

Asst.Engineer

Asst.Executive Engineer

Scanned with CamScanner

BRUHAT BANGALORE MAHANAGARA PALIKE

Name of Work:Improvements to Roads and drains works at Kattigenahalli Main and Cross, Sirinagara, Niranthara layout, SriKrishna Garden, ShivaShankar layout, Varaha layout, Bindu layout and Surrounding areas in Ward No-05

Measurement Sheet

First and Part Bill

Item No: 9

Item Name: Providing and Fixing pre cast covering Slab 250mm thick made out of M25 and jelly 20mm Down size with steel reinforcement including form work,curing,including cost of all materials, labour,hire charges of machinery, loading, unloading, lead and lift,transportation etc ,complete.As per Engineer incharge. (Data Rate)

Measurement recorded on:

SLNO	CHAINAGE Land Mark		NO	L (m)	B (m)	B1 (m)	Avg B (m)	D (m)	QTY	REMARKS	RATE	AMOUNT
	FOR SSM CULVERT											
	Sri Krishna Garden Main road RHS											
	62.00	69.50	1	7.50	1.50	1.50	1.50		11.25			
	107.60	114.60	1	7.00	1.50	1.50	1.50		10.50			
	140.40	147.40	1	7.00	1.50	1.50	1.50		10.50			
	172.60	178.10	1	5.50	1.50	1.50	1.50		8.25			
	Kattigenahalli 2nd main road											
	0.00	4.20	1	4.20	1.50	1.50	1.50		6.30			
								Total Qty Work Done	**46.80**	**Sqm**		
								Qty Payable in this bill	**46.80**	**Sqm**	**5688.00**	**266198.40**

NEWZEN CONSULTANT ★ Bangalore ★

Consultant Representative

Contractor Representative

9/11/2020

Asst. Executive Engineer

ಬಿ.ಬಿ.ಎಂ.ಪಿ ಬ್ಯಾಟರಾಯನಪುರ ಉಪ ವಿಭಾಗ

BRUHAT BANGALORE MAHANAGARA PALIKE										
Name of Work:Improvements to Roads and drains works at Kattigenahalli Main and Cross, Sirinagara, Niranthara layout, Sri Krishna Garden, ShivaShankar layout, Varaha layout, Bindu layout and Surrounding areas in Ward No-05										
Measurement Sheet										
First and Part Bill										
Item No:	**10**									
Item Name:	KSRRB M300-14. Excavation for roadwork in soil with hydralic excavation of 0.9cum bucket capacity including cutting and loading tippers, trimming bottom and side slopes, in accordance with requirements of lines, grades and cross section , and transportating to the embankment location to a lead of 1 km and complete as per									
SLNO	CHAINAGE Land Mark	NO	L (m)	B (m)	D (m)	QTY	REMARKS	RATE	AMOUNT	
	Vide Premeasurement Page no.					6382.27				
	Qty Payable in this bill					**6382.27**	**Cum**	**60.00**	**382936.32**	
Item No:	**11**									
Item Name:	Construction of granular sub-base Grading-V as Sub-base and drainage layer by providing coarse graded crushed stone aggregates of granite/trap/basalt material, mixing in a mechanical mix plant at OMC , Carriage of mixed materials to work site, spreading in uniform layers with motor grader on prepared surface and									
SLNO	CHAINAGE Land Mark	NO	L (m)	B (m)	D (m)	QTY	REMARKS	RATE	AMOUNT	
	Vide Premeasurement Page no.					3435.03				
	Qty Payable in this bill					**3435.03**	**Cum**	**2095.00**	**7196381.57**	
Item No:	**12**									
Item Name:	KSRRB M400-17. Providing, laying, spreading and compacting crushed stone aggregates of granite / trap / basalt to wet mix macadam specifications including pre mixing the material with water at OMC in mechanical mix plant carriage of mixed materials by tipper to site, laying in uniform layers with paver in sub-base/base course on well prepared surface and compacting with vibratory roller to achieve the									
SLNO	CHAINAGE Land Mark	NO	L (m)	B (m)	D (m)	QTY	REMARKS	RATE	AMOUNT	
	Vide Premeasurement Page no.					4859.82				
	Qty Payable in this bill					**4859.82**	**Cum**	**2101.00**	**10210472.37**	
Item No:	**13**									
Item Name:	KSRRB M500-6. Providing and applying primer coat with S.S. bitumen emulsion on prepared surface of granular base such as WMM including cleaning of road surface and spraying primer at the rate of 0.60 kg / sqm using mechanical means complete as per specifications with all lead and lift and as per the direction of									
SLNO	CHAINAGE Land Mark	NO	L (m)	B (m)	D (m)	QTY	REMARKS	RATE	AMOUNT	
	Vide Premeasurement Page no.					8882.19				
	Qty Payable in this bill					**8882.19**	**Sqm**	**30.00**	**266465.70**	
Item No:	**15**									

ವಿಭಾಗದ ಅಧಿಕಾರಿಗಳು
ಬಿ.ಬಿ.ಎಂ.ಪಿ ಬ್ಯಾಟರಾಯನಪುರ ಉಪ ವಿಭಾಗ

ಸಹಾಯಕ ಕಾರ್ಯನಿರ್ವಾಹಕ ಅಭಿಯಂತರರು
ಬ್ಯಾಟರಾಯನಪುರ ಉಪ ವಿಭಾಗ
ಬಿ.ಬಿ.ಎಂ.ಪಿ., ಬೆಂಗಳೂರು-24

Scanned with CamScanner

SLNO	CHAINAGE / Land Mark	NO	L (m)	B (m)	D (m)	QTY	REMARKS	RATE	AMOUNT
Item Name	KSRRB 500-7. Providing and applying tack coat using 80/100 grade bitumen (VG10) on the prepared black topped surfaces at 2.5 kg per 10 sqm, heating bitumen in boiler fitted with spray set (excluding cleaning of road surface) including cost of all materials, labour, HSM of machineries complete as per								
SLNO	CHAINAGE / Land Mark	NO	L (m)	B (m)	D (m)	QTY	REMARKS	RATE	AMOUNT
	Vide Premeasurement Page no.					8992.19			
	Qty Payable in this bill					8992.19	Sqm	13.00	116896.47
Item No.	16								
Item Name	KSRRB M500-17. Providing and laying Dense Graded Bituminous Macadam using crushed aggregates of specified grading, premixed with VG30 grade bituminous binder and, transporting the hot mix to work site, laying to the required grade, level and alignment, rolling with smooth wheeled, vibratory and tandem rollers to achieve								
SLNO	CHAINAGE / Land Mark	NO	L (m)	B (m)	D (m)	QTY	REMARKS	RATE	AMOUNT
	Vide Premeasurement Page no.					444.11			
	Qty Payable in this bill					444.11	Cum	6926.00	3075002.40

Contractor Representative

Asst Engineer

Consultant Representative

Asst.Executive Engineer

Scanned with CamScanner

BRUHAT BANGALORE MAHANAGARA PALIKE

Name of Work: Improvements to Roads and drains works at Kattigenahalli Main and Cross, Srinagara, Niranthara layout, SriKrishna Garden, ShivaShankar layout, Varaha layout, Bindu layout and Surrounding areas in Ward No-05

Measurement Sheet

First and Part Bill

Item No: 17 — 17/11/2020 to 21/11/2020

Item Name: Providing and laying bituminous concrete 40mm thick with hot mix plant, using crushed aggregates of specified grading, premixed with bituminous binder and filler, transporting the hot mix to work site, laying with a paver finisher to the required grade, level and alignment, rolling with smooth wheeled, vibratory and tandem rollers to achieve the desired compaction in all respects complete as per specifications. Clause 507 of MORTH V revision as per IRC SP- 53-2015 do- using 40-60 TPH capacity HMP with mechanical paver grading II (30-45mm) with 5.4% of modified bituminous binder consisting of 4.97% ofVG-30 bitumen (60/70 grade) and 0.43% of plastomeric thermoplastics (waste plastic) with all lead and lift and as per the direction of Engineer in-charge.

Measurement recorded on:

SLNO	CHAINAGE Land Mark		NO	L (m)	B (m)	B1 (m)	Avg B (m)	D (m)	QTY	REMARKS	RATE	AMOUNT
	Kattigenahalli main road											
	0.00	30.00	1	30.00	10.00	10.50	10.25	0.040	12.30			
	30.00	60.00	1	30.00	10.50	10.70	10.60	0.040	12.72			
	60.00	90.00	1	30.00	10.70	10.70	10.70	0.040	12.84			
	90.00	120.00	1	30.00	10.70	10.80	10.75	0.040	12.90			
	120.00	150.00	1	30.00	10.80	10.10	10.45	0.040	12.54			
	150.00	180.00	1	30.00	10.10	9.70	9.90	0.040	11.88			
	180.00	210.00	1	30.00	9.70	9.10	9.40	0.040	11.28			
	210.00	240.00	1	30.00	9.10	9.30	9.20	0.040	11.04			
	240.00	270.00	1	30.00	9.30	7.10	8.20	0.040	9.84			
	270.00	300.00	1	30.00	7.10	6.90	7.00	0.040	8.40			
	300.00	330.00	1	30.00	6.90	6.50	6.70	0.040	8.04			
	330.00	350.00	1	20.00	6.50	13.00	9.75	0.040	7.80			
	350.00	370.00	1	20.00	13.00	7.60	10.30	0.040	8.24			
	370.00	390.00	1	20.00	7.60	7.00	7.30	0.040	5.84			
	390.00	420.00	1	30.00	7.00	6.80	6.90	0.040	8.28			
	420.00	450.00	1	30.00	6.80	10.00	8.40	0.040	10.08			
	450.00	480.00	1	30.00	10.00	7.00	8.50	0.040	10.20			
	480.00	510.00	1	30.00	7.00	8.50	7.75	0.040	9.30			
	510.00	540.00	1	30.00	8.50	8.10	8.30	0.040	9.96			
	540.00	551.00	1	11.00	6.20	12.80	9.50	0.040	4.18			
	551.00	564.00	1	13.00	15.60	12.60	14.10	0.040	7.33			
	564.00	580.00	1	16.00	12.60	9.40	11.00	0.040	7.04			
	580.00	604.00	1	24.00	9.40	9.00	9.20	0.040	8.83			
	Sri Krishna garden main road											
	0.00	30.00	1	30.00	7.40	7.40	7.40	0.040	8.88			
	30.00	60.00	1	30.00	7.40	7.45	7.43	0.040	8.91			
	60.00	90.00	1	30.00	7.45	7.20	7.33	0.040	8.79			
	90.00	120.00	1	30.00	7.20	7.30	7.25	0.040	8.70			
	120.00	150.00	1	30.00	7.30	7.30	7.30	0.040	8.76			
	150.00	180.00	1	30.00	7.30	7.00	7.15	0.040	8.58			
	180.00	210.00	1	30.00	7.00	6.90	6.95	0.040	8.34			
	210.00	213.00	1	3.00	6.90	6.90	6.90	0.040	0.83			
	Sri Krishna garden cross road A											
	0.00	30.00	1	30.00	7.50	7.00	7.25	0.040	8.70			
	30.00	60.00	1	30.00	7.00	7.70	7.35	0.040	8.82			
	Sri Krishna garden cross road B											
	0.00	30.00	1	30.00	5.80	7.20	6.50	0.040	7.80			
	30.00	60.50	1	30.50	7.20	7.20	7.20	0.040	8.78			

17/11/20 – 21/11/20

Scanned with CamScanner

SLNO	CHAINAGE		NO	L	B	B1	Avg B	D	QTY	REMARKS	RATE	AMOUNT
	Land Mark			(m)	(m)	(m)	(m)	(m)				
	Sri Krishna garden cross road C											
	0.00	30.00	1	30.00	5.60	6.00	5.80	0.040	6.96			
	30.00	57.80	1	27.80	6.00	5.50	5.75	0.040	6.39			
	Sri Krishna garden cross road D											
	0.00	30.00	1	30.00	5.20	5.80	5.50	0.040	6.60			
	30.00	56.80	1	26.80	5.80	5.80	5.80	0.040	6.22			
	Sri Krishna garden cross road E											
	0.00	30.00	1	30.00	5.30	6.10	5.70	0.040	6.84			
	30.00	53.00	1	23.00	6.10	5.90	6.00	0.040	5.52			
								Total Qty Work Done	355.29	Cum		
								Qty Payable in this bill	355.29	Cum	8140.00	2892041.06
									Net Amount			41591084.36
									12% GST			4990930.12
									Grand total Amount			46582014.48

NEWZEN CONSULTANT ★ Bangalore ★

Contractor Representative

Asst Engineer

21/11/22

Consultant Representative

Asst.Executive Engineer

ಸಹಾಯಕ ಕಾರ್ಯನಿರ್ವಾಹಕ ಅಭಿಯಂತರರು

ಬ್ಯಾಟರಾಯನಪುರ ಉಪ ವಿಭಾಗ

ಬಿ.ಬಿ.ಎಂ.ಪಿ., ಬೆಂಗಳೂರು-24

Scanned with CamScanner

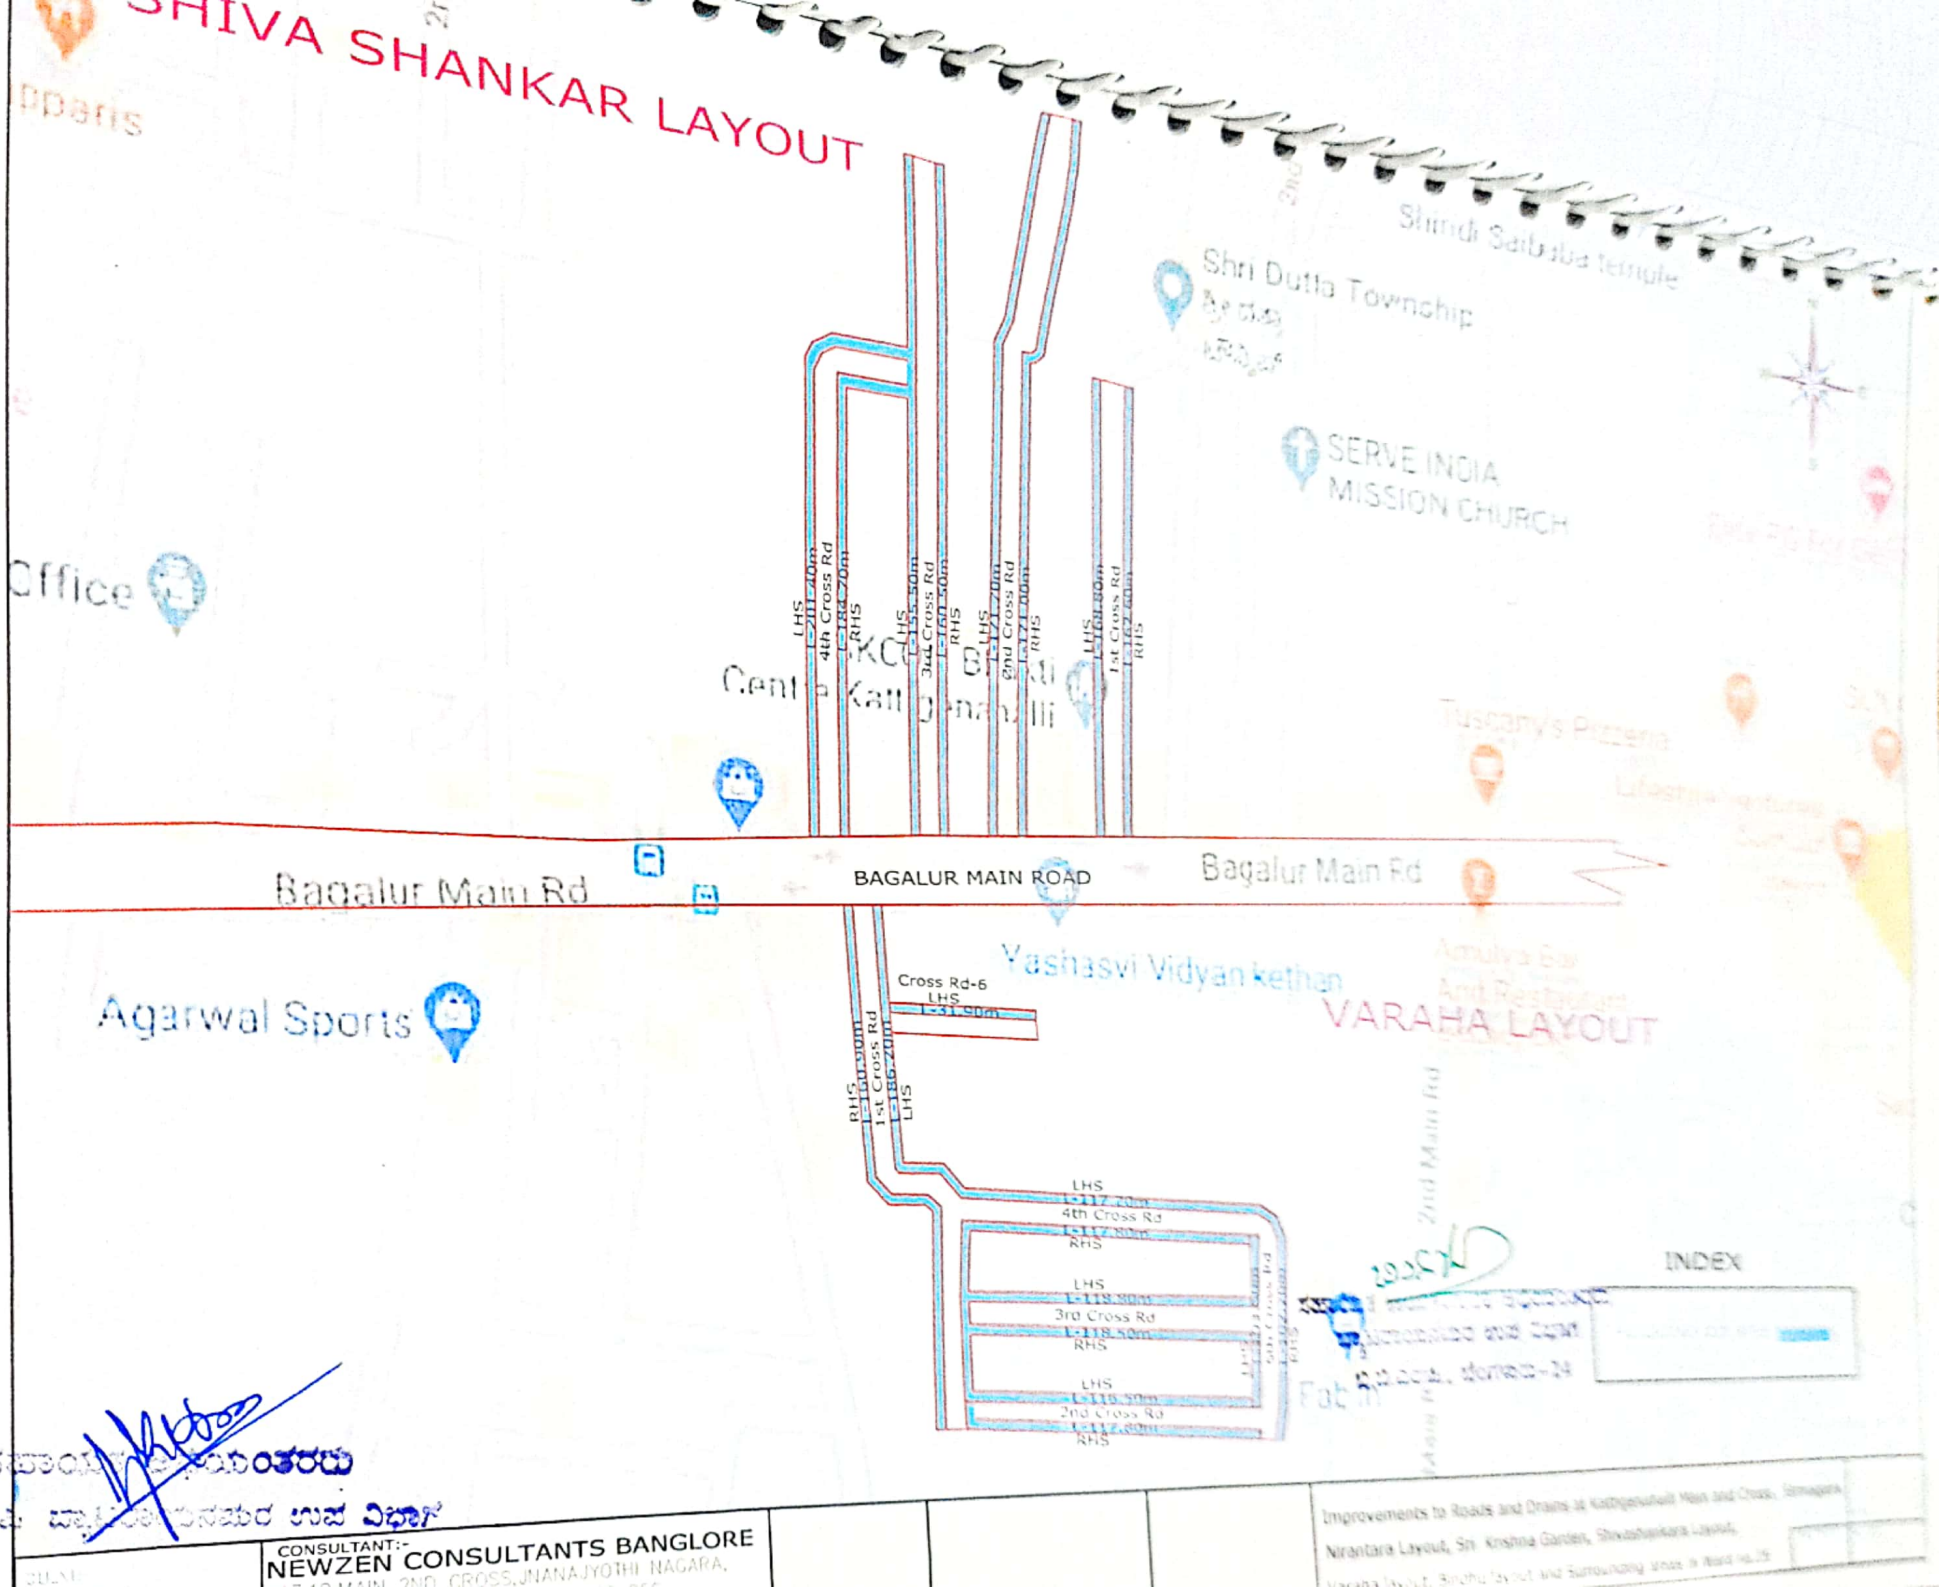

Scanned with CamScanner

SRI KRISHNA GARDEN

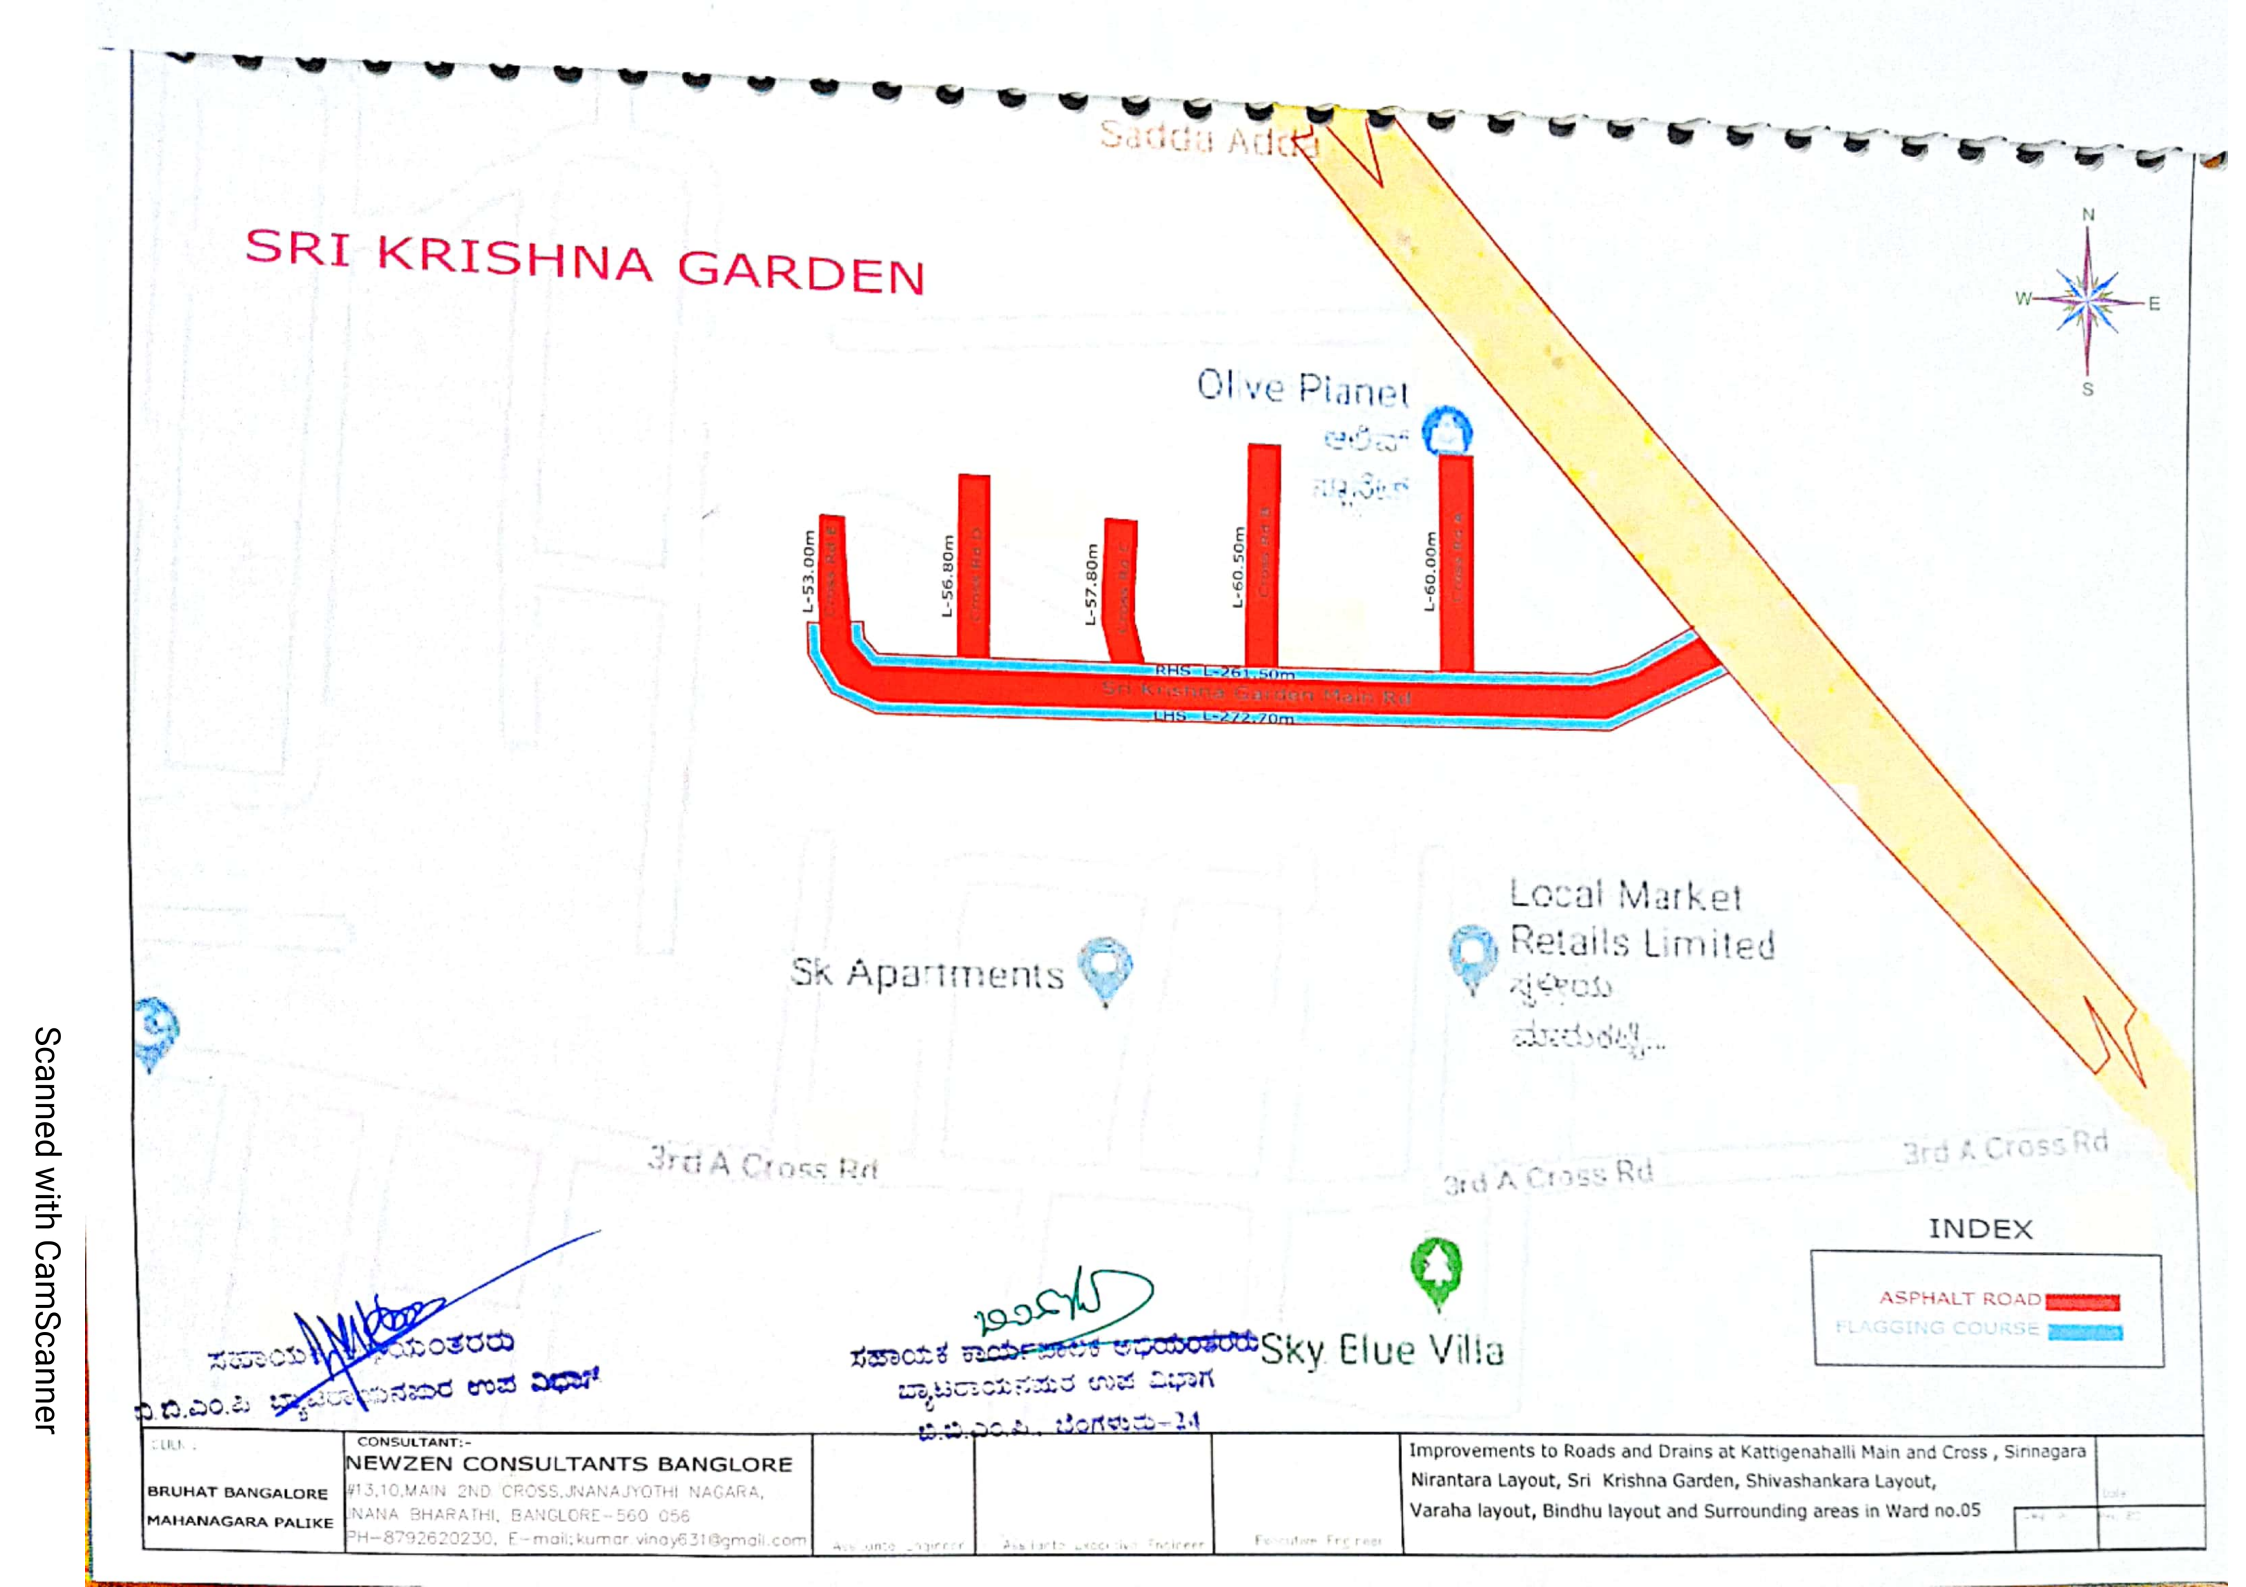

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಬ.ಬ.ಎಂ.ಪಿ ಬ್ಯಾಟರಾಯನಪುರ ಉಪ ವಿಭಾಗ

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಬ್ಯಾಟರಾಯನಪುರ ಉಪ ವಿಭಾಗ
ಬ.ಬ.ಎಂ.ಪಿ, ಬೆಂಗಳೂರು-26

CLIENT:- BRUHAT BANGALORE MAHANAGARA PALIKE	CONSULTANT:- NEWZEN CONSULTANTS BANGLORE #13,10,MAIN 2ND CROSS,JNANAJYOTHI NAGARA, JNANA BHARATHI, BANGLORE-560 056 PH-8792620230, E-mail:kumar.vinay631@gmail.com	Assistant Engineer	Assistant Executive Engineer	Executive Engineer	Improvements to Roads and Drains at Kattigenahalli Main and Cross , Sinnagara Nirantara Layout, Sri Krishna Garden, Shivashankara Layout, Varaha layout, Bindhu layout and Surrounding areas in Ward no.05

Scanned with CamScanner

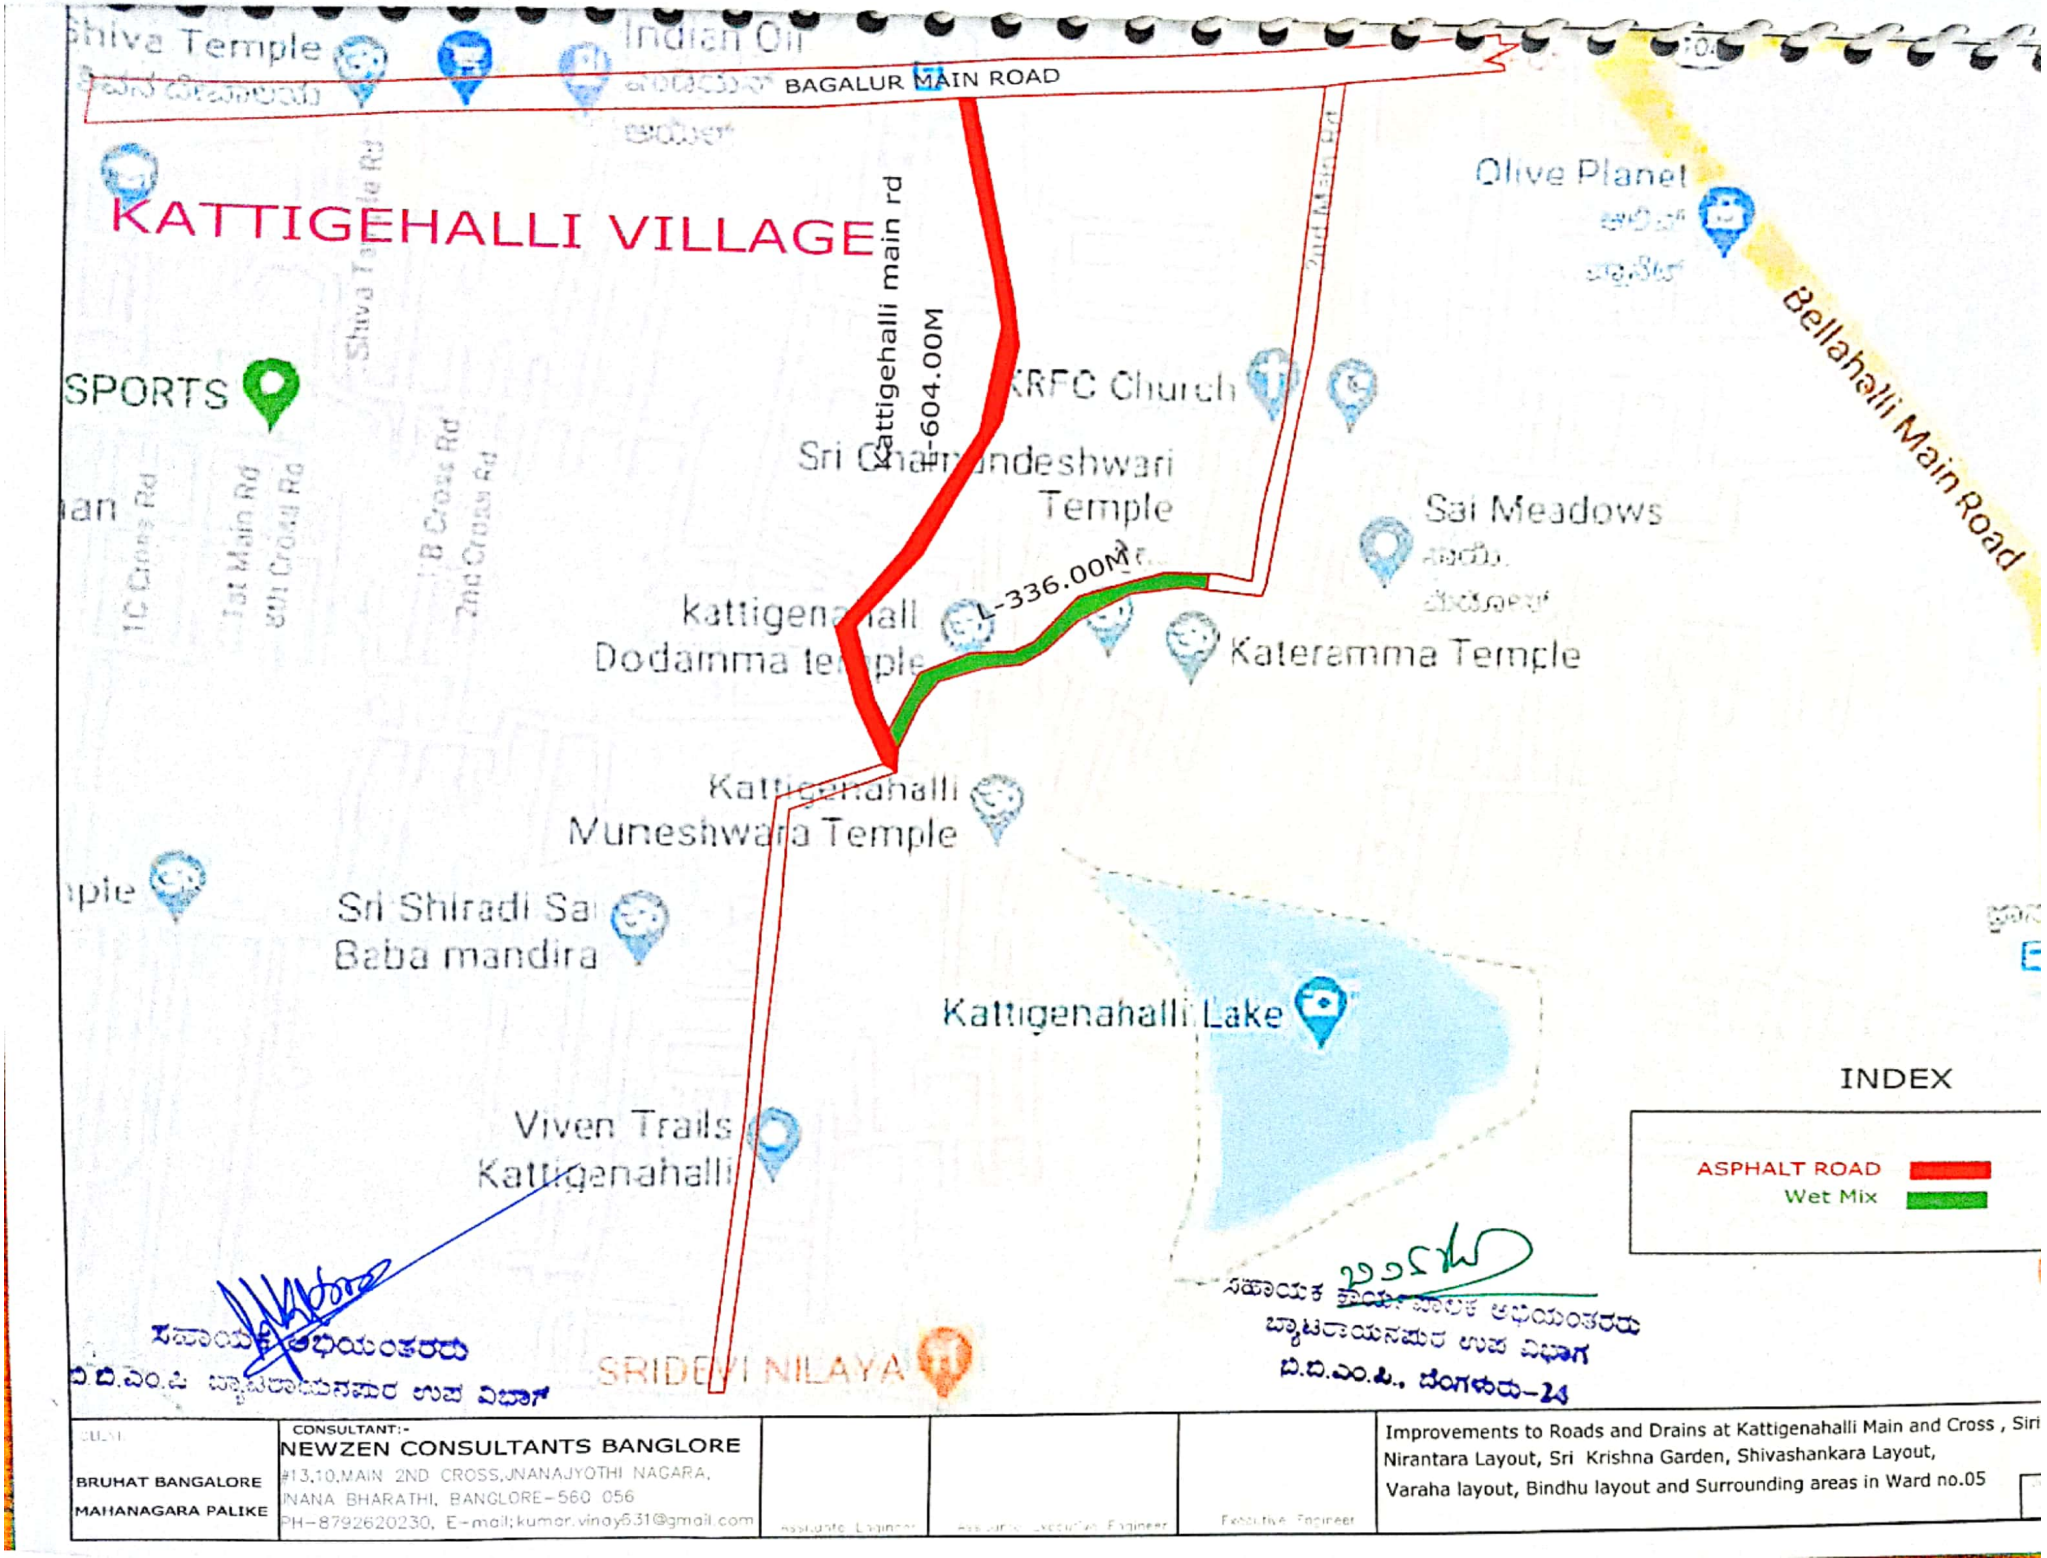

Scanned with CamScanner

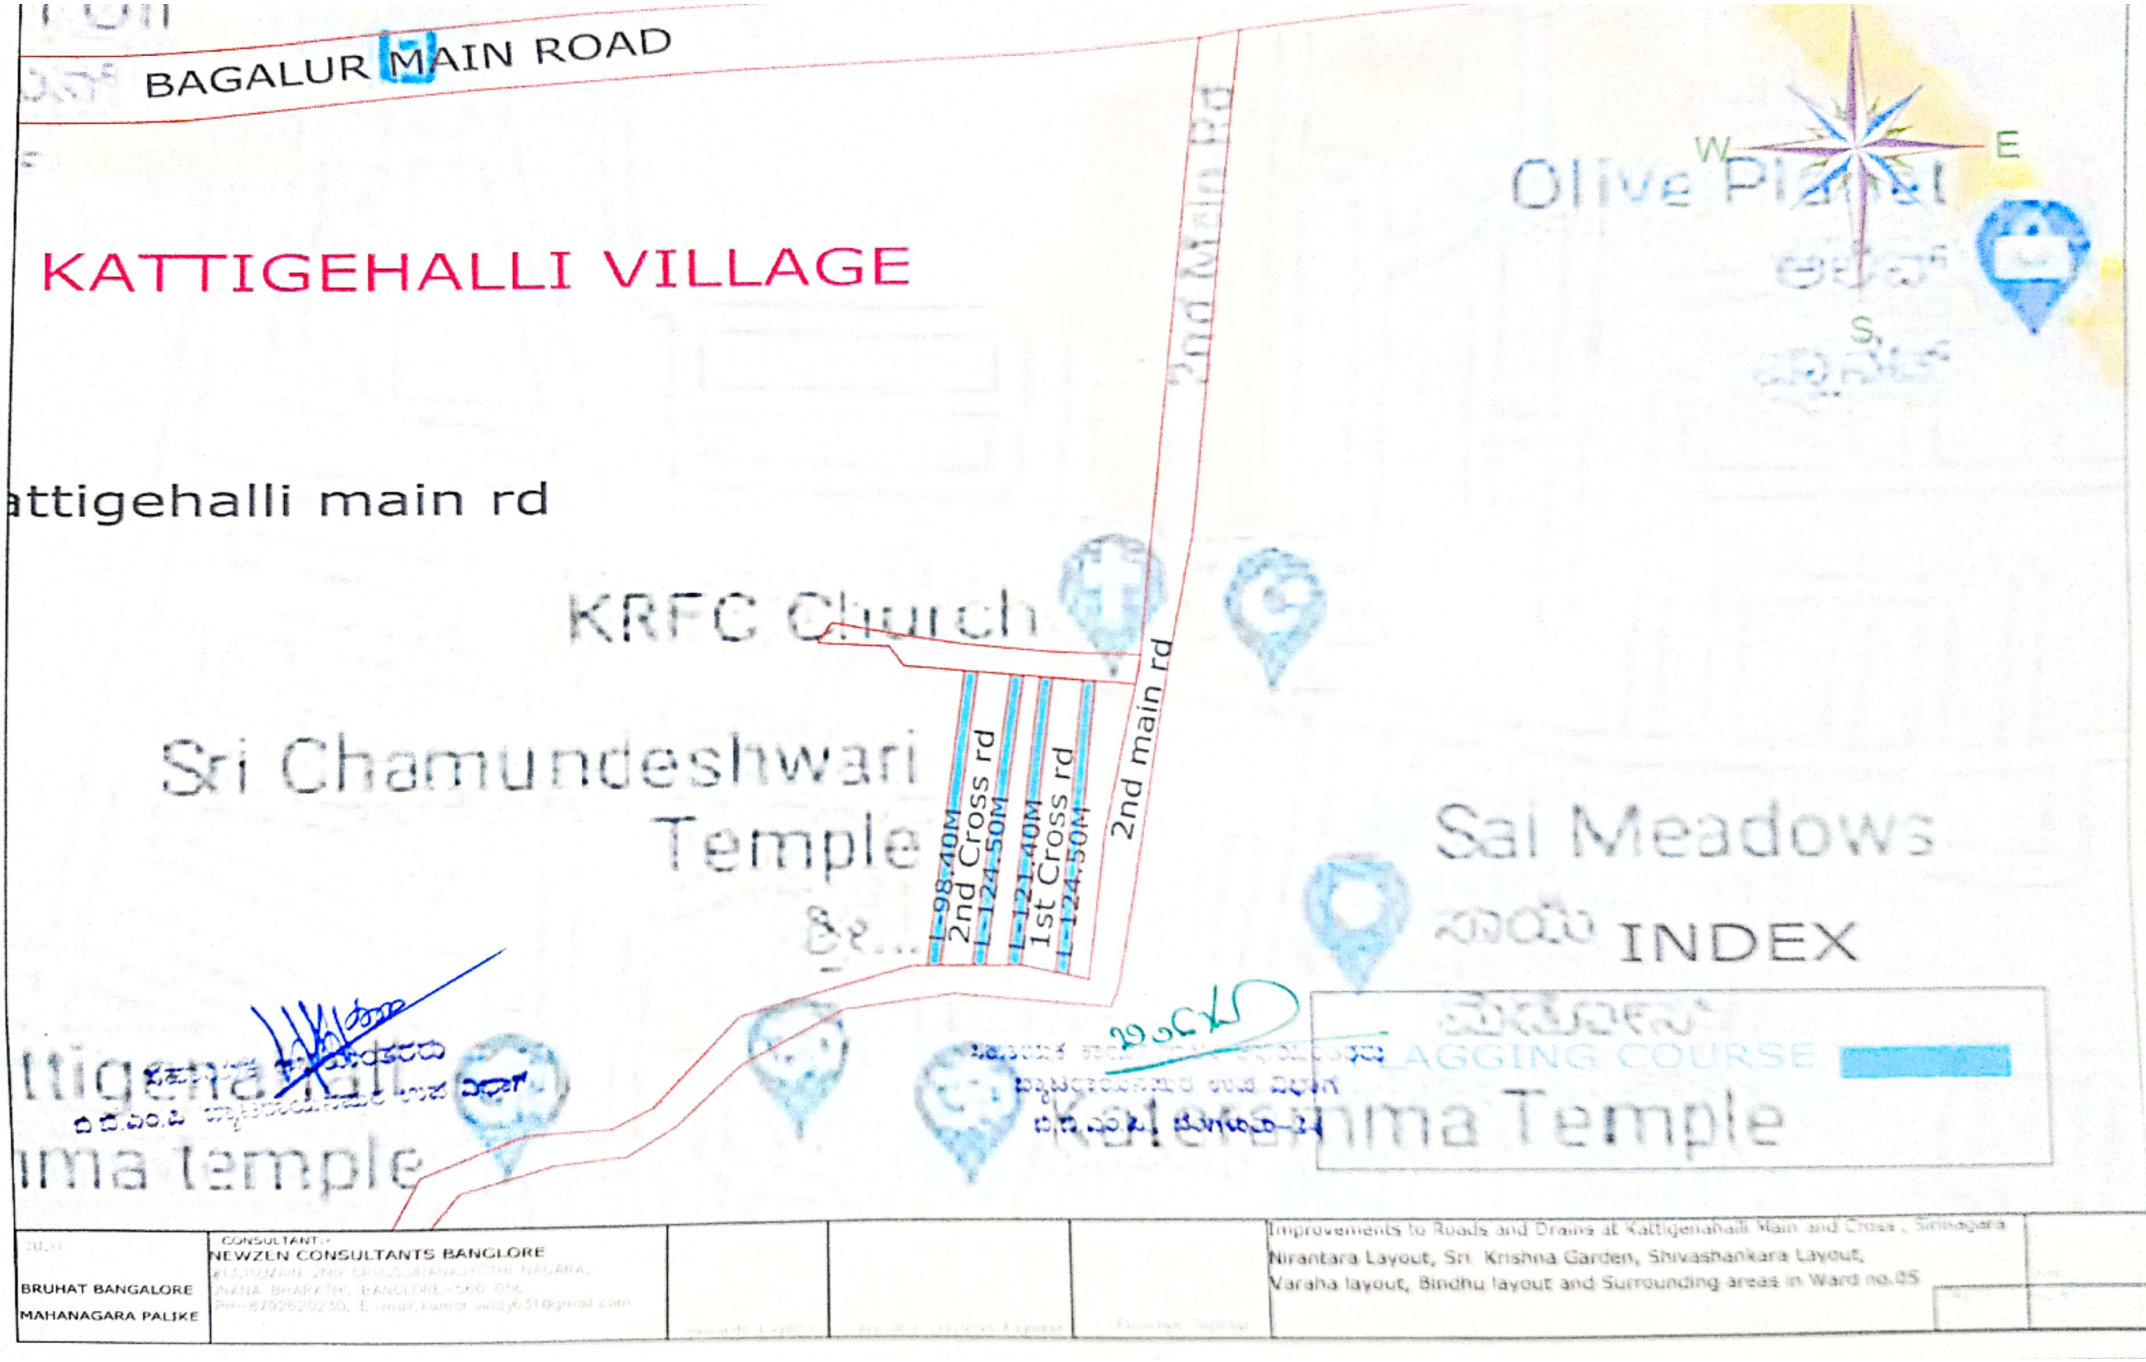

Scanned with CamScanner

BINDHU LAYOUT

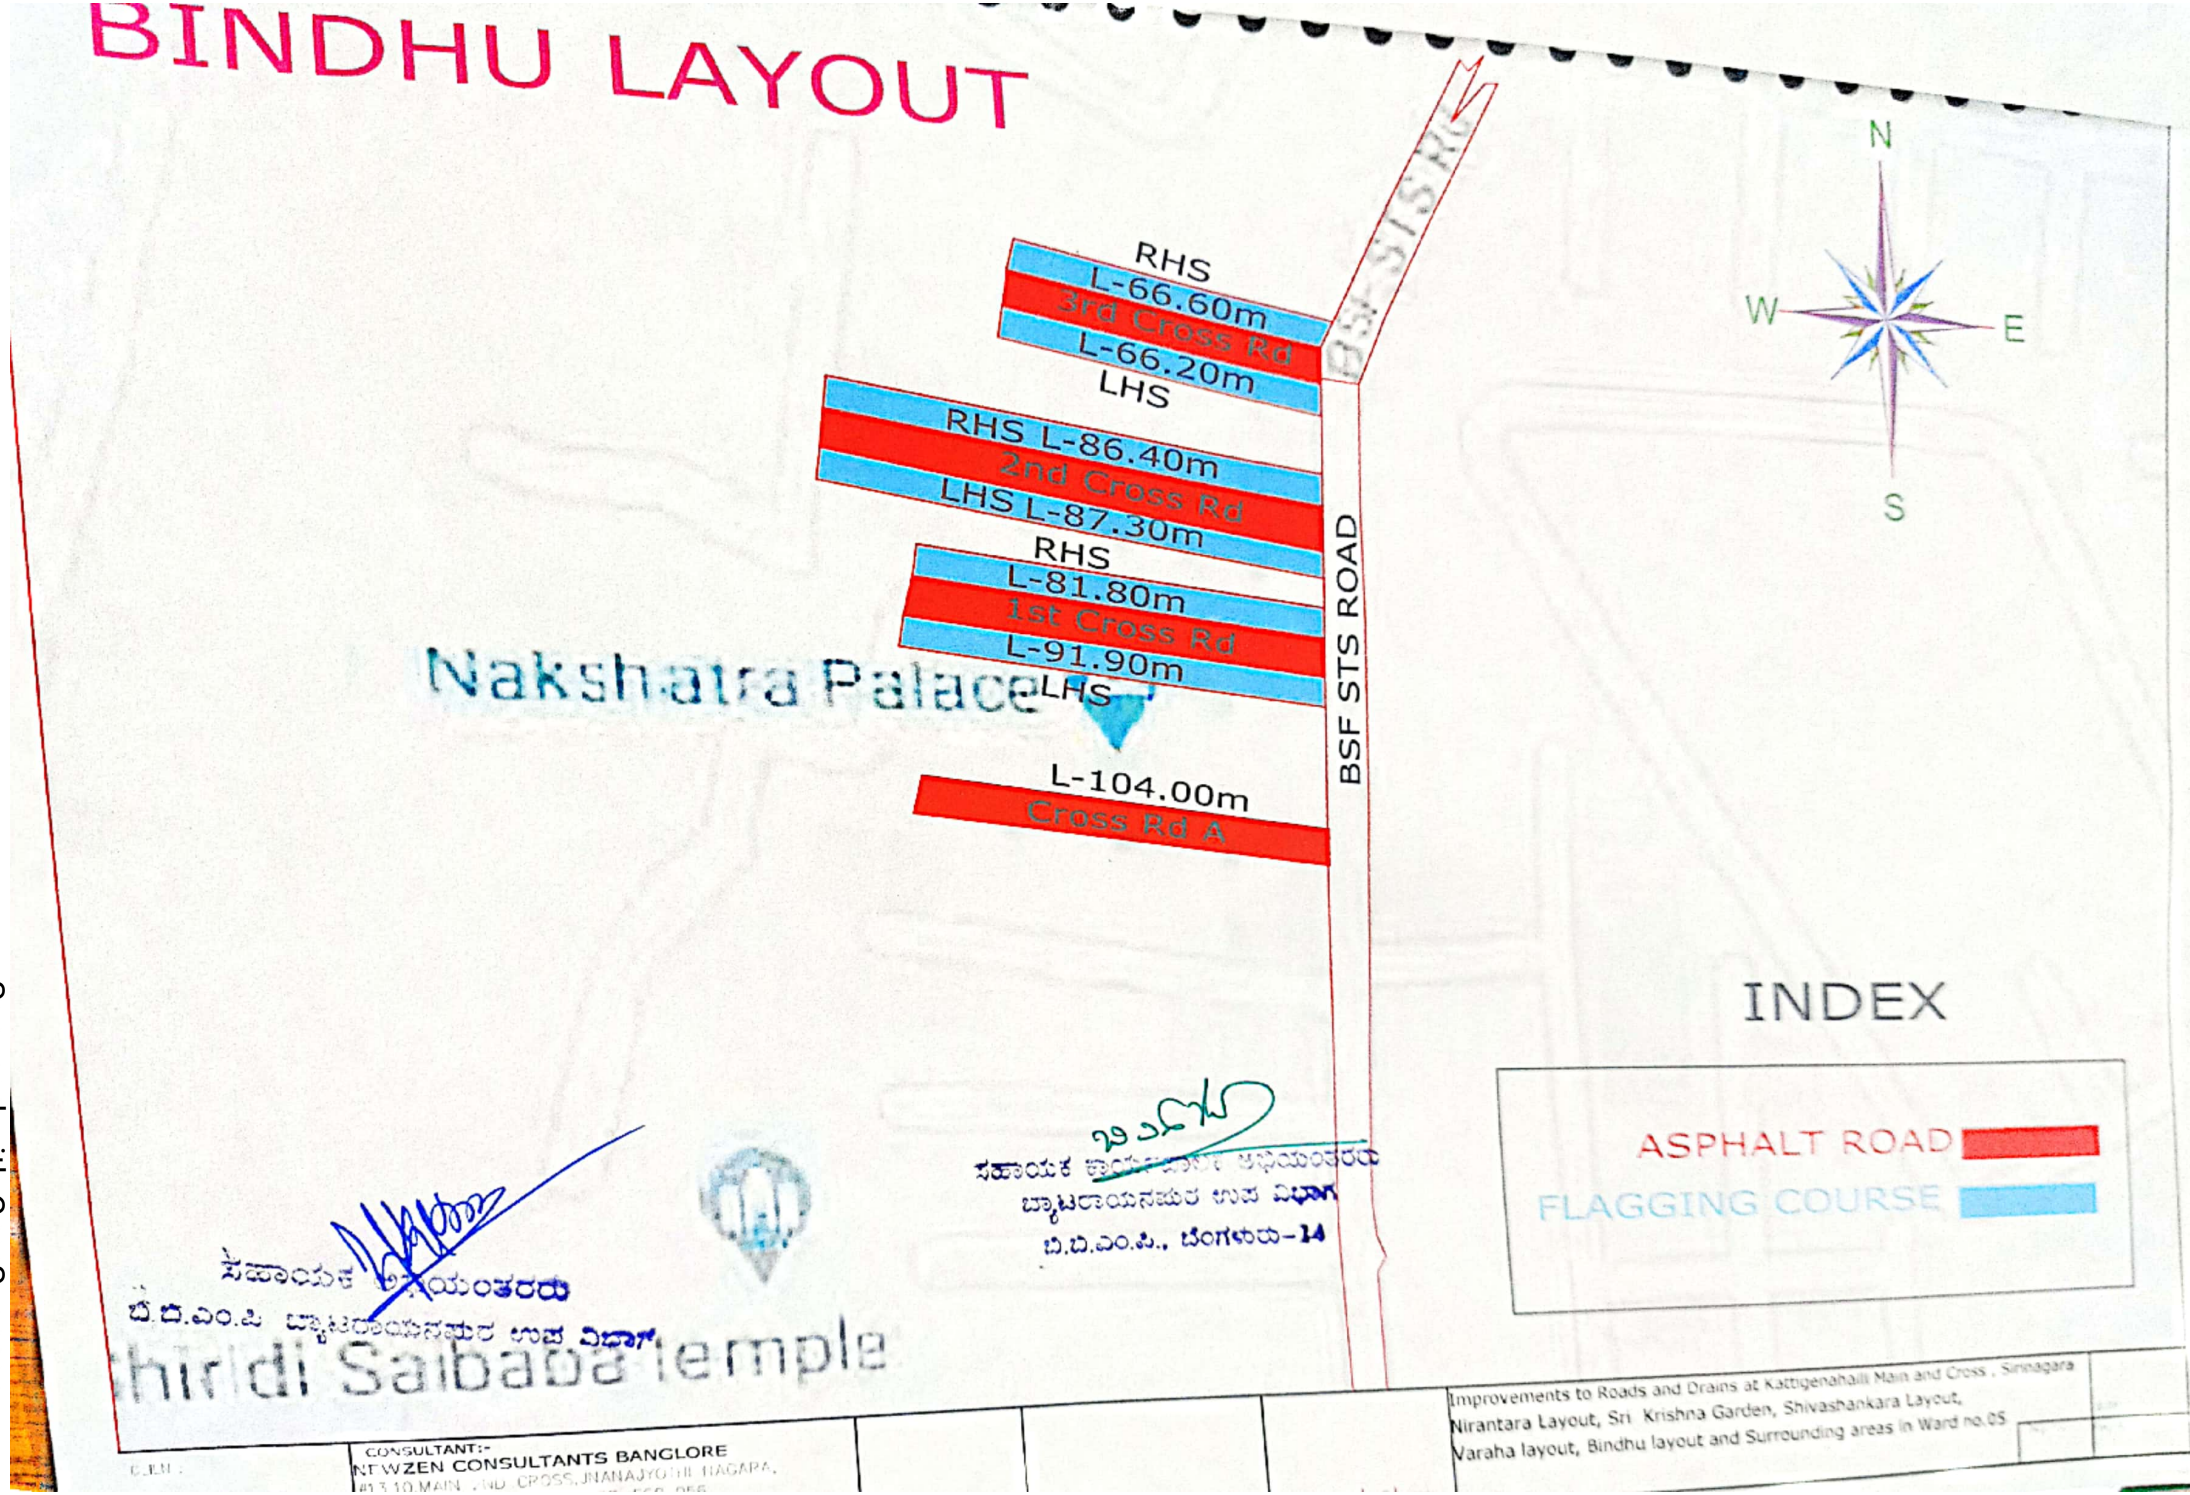

Scanned with CamScanner

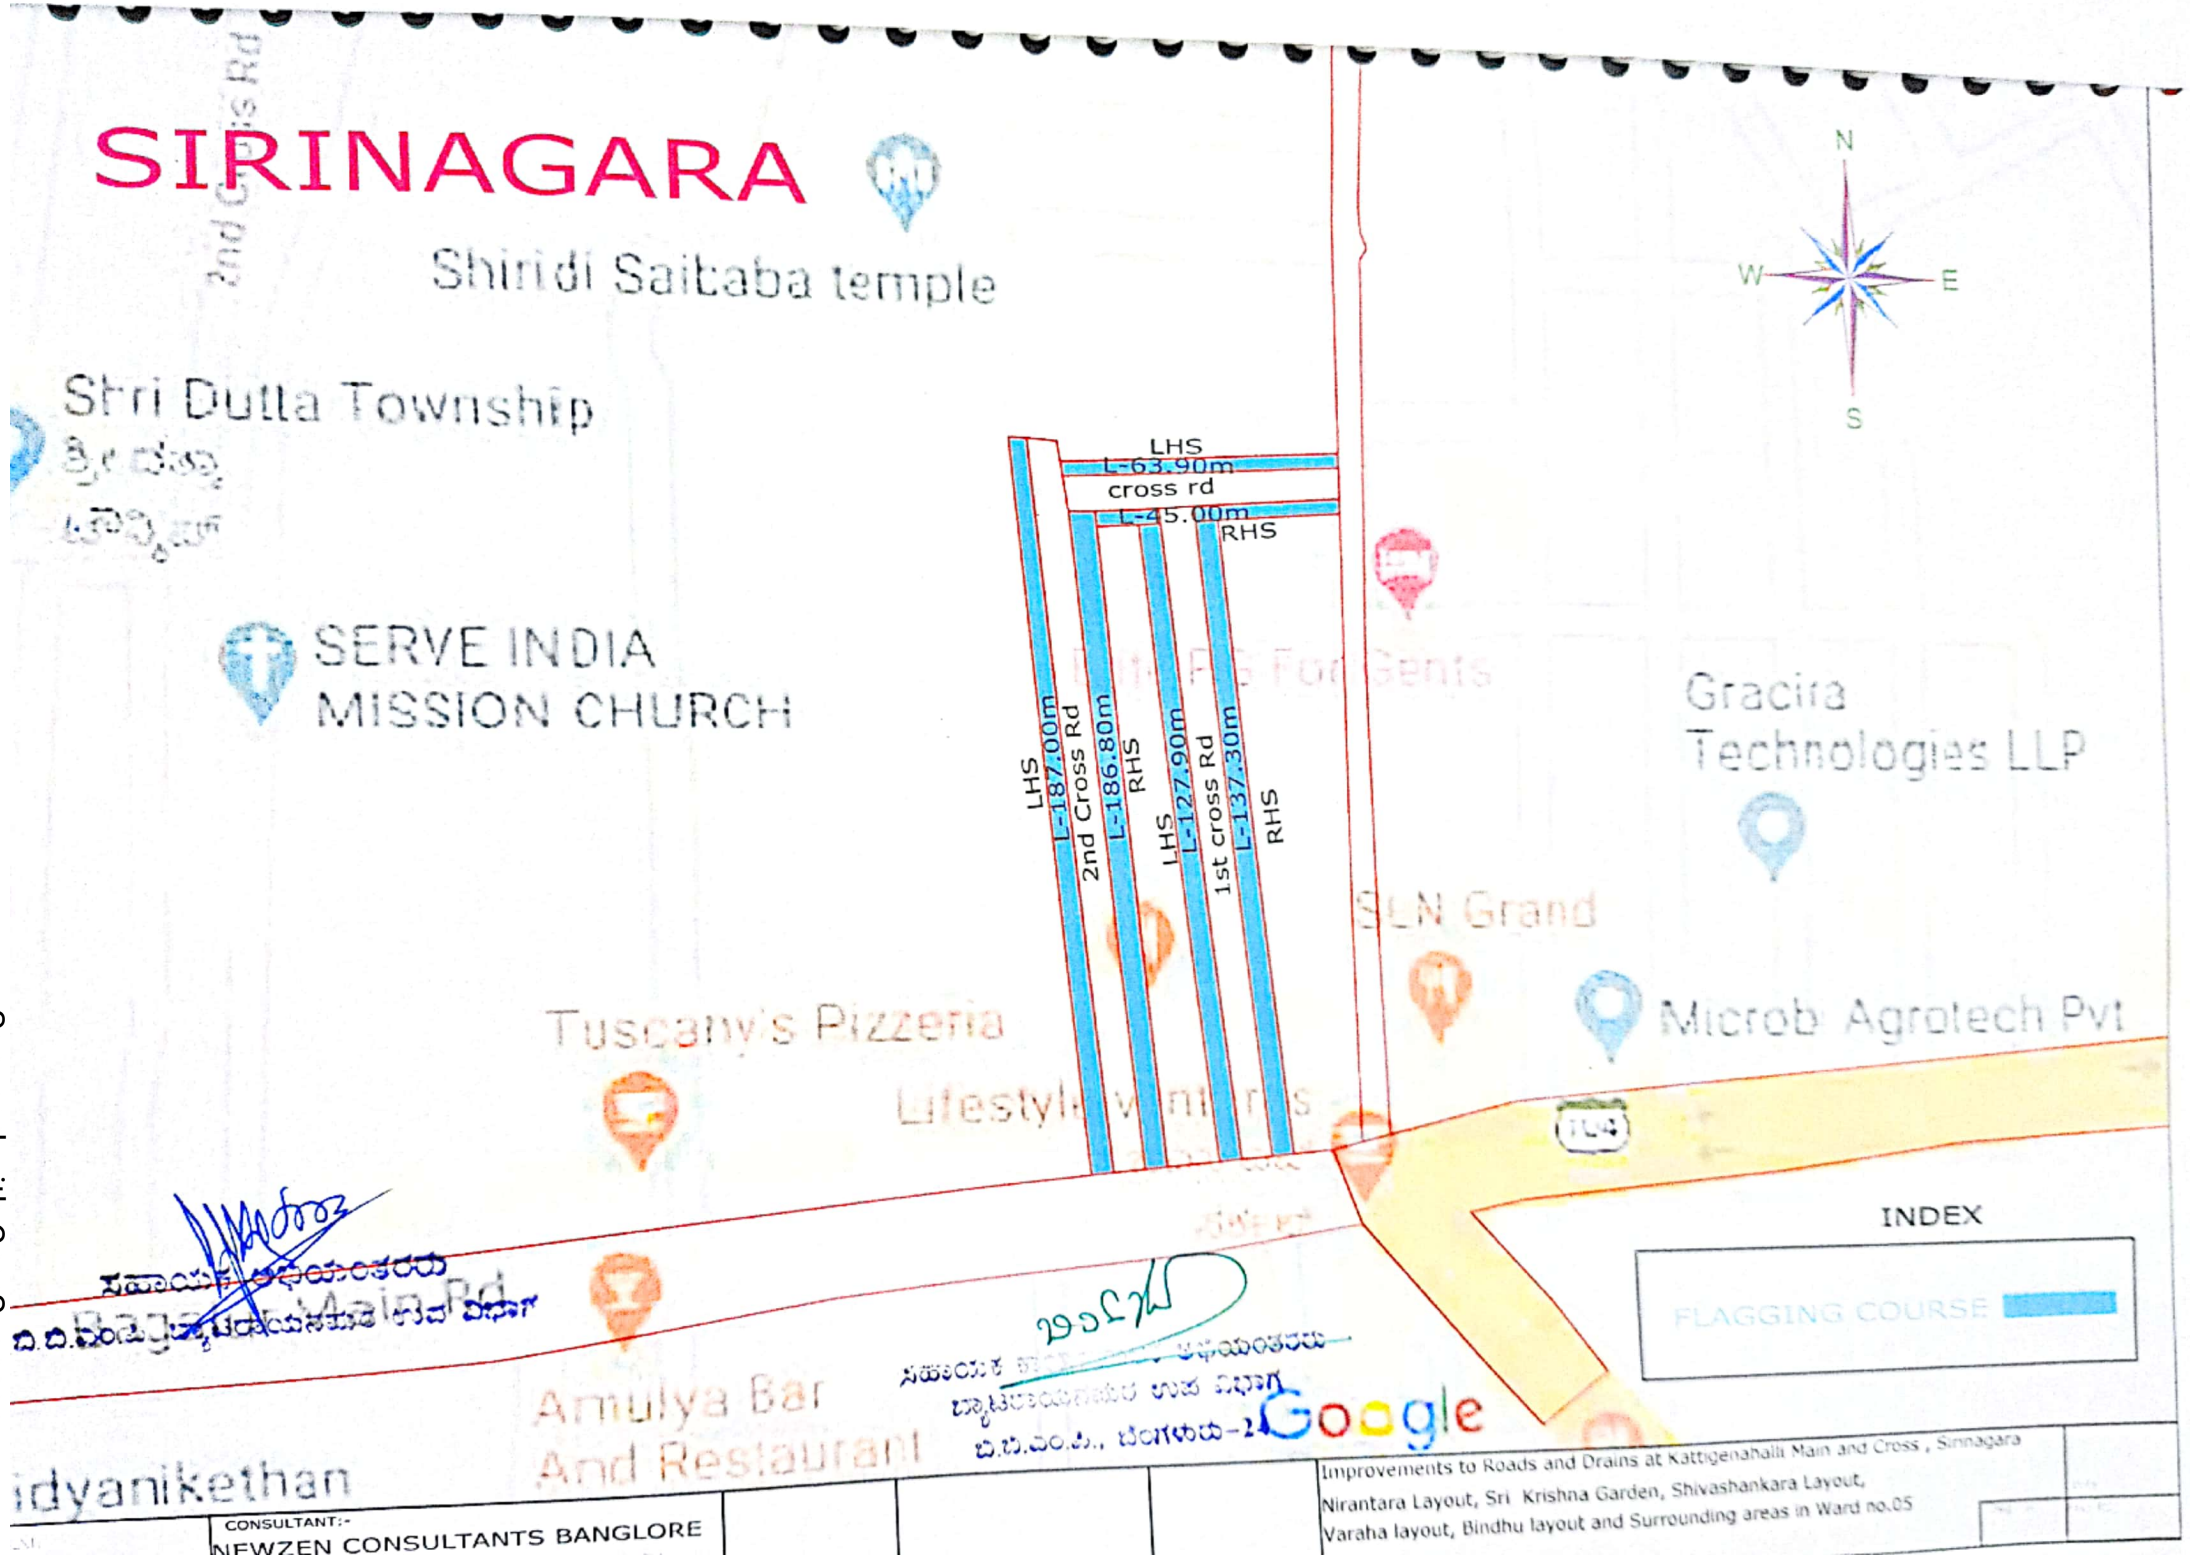

Scanned with CamScanner
